



Social Monitoring Report

PUBLIC

Semestral Report: October 2024 – March 2025
August 2025

India: Rajasthan Secondary Towns Development Sector Project

Prepared by Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited
Externally Aided Projects for the Asian Development Bank (ADB).

Asian Development Bank

This social monitoring report is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of ADB's website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, ADB does not intend to make any judgments as to the legal or other status of any territory or area.

**RAJASTHAN SECONDARY TOWNS DEVELOPMENT SECTOR PROJECT
ASIAN DEVELOPMENT BANK LOAN ASSISTANCE
(LOAN NO. 3972 IND)**

SFG Log: 6643

**SEMIANNUAL SOCIAL SAFEGUARD MONITORING REPORT
(October 2024 to March 2025)**

**Prepared by Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation
Limited Externally Aided Projects for the Asian Development Bank.**

ABBREVIATIONS

ADB	Asian Development Bank
AP	Affected Person
ASO	Assistant Safeguard Officer
BPL	Below Poverty Line
CAPPC	Community Awareness Public Participation Consultant
CBO	Community Based Organization
CCC	Central Control Center
CLC	City Level Committee
CPR	Community Property Resources
CRMC	Consumer Relation Management Center
DMA	District Metering Area
DP	Displace Person
EA	Executing Agency
FGD	Focus Group Discussions
FHH	Female Headed Household
FSTP	Feacal Sludge Treatment plant
GoI	Government of India
GoR	Government of Rajasthan
GRC	Grievance Redressal Committee/ Grievance Redressal Cell
IA	Implementing Agency
IP	Indigenous Peoples
IR	Involuntary Resettlement
LAA	Land Acquisition Act
RFCT LARR	The Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement Act
M&E	Monitoring and Evaluation
NGO	Non-Government Organizations
NPRR	National Policy on Resettlement & Rehabilitation
PIU	Program Implementation Unit
PH	Physically Handicapped
PMCBC	Project Management Capacity Building Consultants
PMU	Program Management Unit
RoW	Right of Way
RF	Resettlement Framework
RP	Resettlement Plan
RIPP	Resettlement and Indigenous Peoples Plan
R&R	Resettlement & Rehabilitation
RUIDP	Rajasthan Urban infrastructure Development Project
RSTDSP	Rajasthan Secondary Towns Development Sector Project
SC	Scheduled Caste
SIA	Social Impact Assessment
SIP	Service Improvement Plan
SOT	Social Outreach Team (Contractor's Outreach team)
ST	Scheduled Tribe
STD	Sexually Transmitted Diseases
SwPS	Sewerage Pumping Station
ToR	Terms of Reference
UDD	Urban Development Department
VC	Valuation Committee

CONTENTS

EXECUTIVE SUMMARY	1
A. PROJECT BACKGROUND AND DESCRIPTION	6
B. PURPOSE OF THE REPORT	10
C. SOCIAL SAFEGUARD CATEGORIZATION	10
D. STATUS OF PREPARATION/ UPDATING OF RPs/RIPPs	12
E. IMPLEMENTATION OF RESETTLEMENT PLAN	13
F. CURRENT STATUS OF RP – IMPLEMENTATION	14
G. CURRENT STATUS OF FSSM.....	19
H. PUBLIC PARTICIPATION AND CONSULTATION.....	20
I. CAPACITY BUILDING ACTIVITIES OF PROJECT IMPLEMENTING AGENCIES	22
J. GRIEVANCE REDRESS MECHANISM	22
K. INSTITUTIONAL ARRANGEMENT	24
L. MONITORING RESULTS-FINDINGS.....	28
M. COMPLIANCE STATUS OF LOAN COVENANTS.....	30
N. FOLLOW UP ACTIONS, RECOMMENDATION AND DISCLOSURE.....	33

Table

Table 1: Summary of Proposed Improvements in Project Towns.....	7
Table 1(A): Description of the subprojects	8
Table-2: Details of Social Safeguard Documents	13
Table 3: No. of APs reported as per socio-economic survey	15
Table 4: Number of affected persons Paid Assistance	16
Table 5: Status of payment to affected persons	16
Table 6: Details of affected persons mitigated up to March 2025.....	17
Table 7: Summary of Consultations in Project Towns	21
Table 8: Toll free number in each project towns	23
Table 9: Deployment Status of Social Safeguards officials during the Reporting Period	25
Table 10: Mobilization of Nodal officers at PIUs level	26
Table 11: Present Status of SOT	27
Table-12: Status of Monitoring of the Sub-projects (October 2024 – March 2025)	28
Table 13: Status of Loan Covenants	30
Table-14: Issues and Recommendations.....	33

Figure

Figure 1: Location of project towns-RSTDSP	7
Figure02: Grievance Redress Mechanism-RSTDSP	24

Appendix

Appendix 1: Progress and Status of Subproject- RSTDSP.....	34
Appendix 2: Details of Payment Disbursed During this Reporting Period	35
Appendix 3: Photographs of Identity Card Distribution to Affected Persosns	42
Appendix 4: Ward-wise population Schedule Tribe towns	44
Appendix 5: Photographs of civil work under FSSM towns.....	47
Appendix 6: Details of consultation with stakeholder & community people	51

Appendix 7: Photographs of activities performed under Gender Action Plan	73
Appendix 8: Copy of office order of PMU for follow grievance mechanism agreed with ADB	77

EXECUTIVE SUMMARY

The Rajasthan Secondary Towns Development Sector Project (RSTDSP) is the fourth phase of investment projects financed by the Asian Development Bank (ADB) and implemented by the Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited-Externally Aided Projects (RUDSICO-EAP), previously known as Rajasthan Urban Infrastructure Development Project (RUIDP). RSTDSP aims to improve water supply, sewerage and other infrastructure services in secondary towns of Rajasthan with populations ranging from 20,000-1,15,000 through a sector loan modality. The project is aligned with the following impact(s): (i) improvement in access to potable, affordable, reliable, equitable, and environmentally sustainable drinking water supply in all urban areas of Rajasthan, (ii) improvement in the health status of the urban population, especially the poor and underprivileged through improvements in sewerage systems of sub-project towns (iii) improvements in other infrastructure services of some towns. Under RSTDSP, work is in progress in 14 project towns. From the savings under the ongoing project of RSTDSP, the Government of Rajasthan (GoR) has decided to implement Faecal Sludge and Septage Management (FSSM) through the construction of FSTPs in selected 13 towns that do not have a central sewer network. The project is expected to increase operational efficiency, improve service delivery, and positively impact health and quality of life for the residents of project towns in the State.

Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited (RUDSICO) is the implementing Agency (IA) for the project. The Project Management Unit (PMU) is headed by Project Director. Social Project Officer (SPO) at PMU assisted by Safeguard Specialist-Resettlement of Project Management Capacity Building Consultant (PMCBC) to ensure that all subprojects meet safeguard requirements as agreed in the loan covenant and in line with this resettlement framework (RF). Project implementation Units (PIUs) are headed by the superintending engineer/executive engineer for the implementation of the project. One Engineer in each PIUs has been designated as a safety and safeguard officer who is responsible for safeguard and health and safety requirements, monitoring, and compliance. PIU is supported by a Social safeguard cum Gender Professional Construction Management Supervision Consultant(CMSC) in all areas of project implementation, implementation of resettlement plan and safeguard monitoring and compliance.

The current report is the 8th semiannual social safeguard monitoring report (SSMR) prepared for the reporting period from October 2024 to March 2025. The general objective of this Semiannual Social Safeguard Monitoring Report (SSMR) is to assess the progress on safeguard measures taken during the reporting period.

Draft resettlement plans (RPs) for eight subprojects¹ and draft Resettlement and Indigenous Peoples Plans (RIPPs) for three subprojects² were prepared for the 11 selected project cities/towns during the loan processing stage. For three subprojects³, where no involuntary resettlement (IR) impacts were envisaged during the initial assessment, due diligence reports (DDRs) have been prepared as per SPS, 2009. All resettlement plans (RPs) and resettlement and indigenous peoples plans (RIPPs) prepared during the loan processing phase are being revised by CMSC and PMCBC during implementation. Accordingly, a resettlement framework (RF) was also prepared to guide RSTDSP on Involuntary Resettlement (IR) impacts during project implementation. All RIPPs and RPs are being updated based on a detailed measurement survey (DMS), approved design and alignment, 100% census, and socio-economic survey of potentially affected persons (APs) and are being submitted to ADB.

From the savings under the ongoing project of RSTDSP, the Government of Rajasthan (GoR) has decided to implement Faecal Sludge and Septage Management (FSSM) through the construction of FSTPs in selected 13 towns⁴ that do not have a central sewer network. The project is expected to increase operational efficiency, improve service delivery, and positively impact on health and quality of life for the residents of project towns in the State. Screening and impact assessment was done by the team of detailed project report (DPR) consultants, safeguard consultant, and staff from Urban Local Bodies (ULBs) in all 13 towns and it was confirmed that all the proposed works have no involuntary resettlement impacts. For location change of FSTPs at Bari, Deeg, Shahpura (Jaipur) & Pilibanga-Suratgarh, Due Diligence Reports (DDRs) of all four towns have been updated, and the same have also been approved by ADB. At present all the DD Rs of 13 towns have also been updated and approved by the ADB.

It is confirmed that all subprojects do not cause (i) any significant involuntary resettlement (IR) impacts or/ and (ii) impact on indigenous people (IP). The construction of the sub-project does not require any acquisition of land or cause permanent displacement, except for Fatehpur and Makrana town, where a small portion of private lands has been purchased by the Municipality through negotiated settlement for the construction of sewerage pumping stations (SPS). At Kuchaman water supply and waste water subproject the proposed land (425 sq meter) for SPS 3.1 MLD, has been obtained under exchange of land parcel. Due diligence has been done and has been reported to ADB using the updated RP and previous SSMR. The locations for the permanent site (sewerage treatment plants (STP), water treatment plants (WTP), sewerage pumping stations, (SPS) Consumer Relation Management Centers (CRMC), Central Control Center (CCC) etc.) have been carefully selected and

¹ Sirohi, Sardarsahar, Laxmangarh, Ratangarh, Khetri, Mandawa, Kuchaman, Ladnu.

² Abu Road, Pratapgarh and Banswara.

³ Fatehpur, Makrana and Didwana

⁴ Bari (Dholpur), Deeg (Bharatpur), Pilibanga (Hanumangarh), Suratgarh (Sri Ganganagar), Shahpura (Bhilwara), Bhinder-Kanod (Udaipur), Gangapur (Bhilwara), Bhawani Mandi (Jhalawar), Dausa, Tijara (Alwar), Bandikui (Dausa), Jobner (Jaipur), Neem Ka Thana (Sikar) and Shahpura (Jaipur).

proposed in the vacant encumbrance free government land. Some lands belonging to gaushala (cow shelter) trusts and government land classified as pasture lands have been obtained, following due procedures required by the government.

In addition to that, during the social impact assessment of the proposed components of the Sirohi subproject, it was noticed that municipal land proposed for STP-1 (near Nehru Nagar), was being used for farm cultivation by one family, and they have faced the permanent loss of agricultural livelihood. The affected family has already been compensated by the project implementation unit (PIU) for their losses and has also been reported to ADB through the previous Semiannual Social Monitoring Report (SSMR).

The main resettlement impact may be the potential reduction in the income of vendors/hawkers operating in the right of way (RoW) during execution. Based on a detailed measurement survey (DMS), approved design and alignment, 100% census / socio-economic survey of potential affected persons, a total **3221** vendors/hawkers were identified (Abu Road-435, Sirohi-349, Sardarsahar-412, Ratangarh-287, Laxmangarh-201, Pratapgarh-412, Banswara-391, Mandawa-77, Khetri-42, Ladnu-252, and Kuchaman-363), among **1286** comes under vulnerable category⁵. As per agreed entitlement matrix, disbursement of compensation against the livelihood losses, shifting/ vulnerability assistance, and escalation against delay in payment as defined in resettlement framework (RF) with respect to cut off date are being made prior to start of any civil work in the affected areas. The sub-projects under Loan 3972-IND has been categorized as 'B' for involuntary resettlement (IR) and 'B'⁶ for Indigenous People (IP) in accordance with the ADB's SPS 2009, which applies to this project.

Out of 14 towns, three towns (Abu Road, Pratapgarh and Banswara) have been declared as a scheduled area by the Government of India. Many Scheduled Tribe (ST) households residing in these three towns no longer maintain their cultural traditions and have settled amongst the non-tribal populations. The subprojects are expected to have beneficial impacts on scheduled tribe community in these three towns- 100% of the scheduled tribe community in coverage areas will be provided with water supply and sewerage connections. In compliance to the action plan, consumer survey has been completed by the project contractors in all the three towns and number of scheduled tribes households in each town has been obtained for providing 100% water supply and sewerage facilities. Several round of consultations done with scheduled tribe households in these towns. The project scope and advantages were disseminated to them. Community awareness activities under GESI

⁵ Vulnerable households comprise below poverty line households, female-headed households, households with out of school/working children, disabled person-headed household, elderly headed household, landless household, household with no legal title/tenure security, and schedule caste and scheduled tribe households.

⁶ Three towns Abu Road, Pratapgarh and Banswara has been declared as a scheduled area by the Government of India.

(Gender Equality Social Inclusion)-action plan have been administered through CAPP consultants. Gender Action Plan involves- developing IEC materials, providing skill training, formation of groups, linkage with livelihood scheme, women internship program etc.

Contracts for all the 14 towns have been awarded, and pipe laying work for wastewater and water supply networks has progressed considerably in all the towns. Construction of FSTPs is also being carried out at a fast pace, except in Shahpura (Jaipur); due to public protest against newly allotted land, work could not be started till the end of this reporting period.

By the end of this reporting period, disbursement of resettlement assistance has been completed in Abu Road, Sirohi, Ratangarh, Laxmangarh, Sardarshahar, Pratapgarh, Banswara, Mandawa, Khetri, and Ladnu. Resettlement assistance of 15 potential affected persons is pending in Kuchaman only due to pending of pipe laying work in APs area. The resettlement assistance of ₹ **1,94,21,284** has been paid to **2033** affected persons (APs)- (Abu Road- 306 (₹3519738), Sirohi-269 (₹2754084), Laxmangarh-98 (₹795710), Pratapgarh-219 (₹1850538) Banswara-290 (₹3209814), Ratangarh-123 (₹999702), Sardarshahar-166 (₹1297598), Mandawa-57 (₹594000), Khetri-32 (₹275100), Ladnu-195 (₹1540600) and Kuchaman-278 (₹2584400), while **41** affected persons (Laxmangarh (17), Ratangarh (01), Abu-road (01), Sardarshahar (07), Pratapgarh (03), Mandawa (02), Ladnu (05) and Kuchaman (05)) are not voluntarily inclined to receive compensation. A total **708** affected persons (Abu-road (128), Sirohi (80), Ratangarh (111), Laxmangarh (29), Sardarshahar (89), Pratapgarh (62) Banswara (74), Mandawa (18), Khetri (10), Ladnu (42) and Kuchaman (65)) are under the missing category (those who were available on the site at the time when construction was undertaken). Up to this reporting period, impacts on **424** affected persons (Sardarsahar (150), Ratangarh (52), Laxamangarh (57), Banswara (27), Pratapgarh (128), and Ladnu (10)) were avoided/ mitigated as worked were executed on one segment at the time, on one side of the road, and access was made available for the roadside petty businesses.

Social Safeguard Support staff posted at CMSCs and concerned towns are conducting regular due diligence of ongoing works & execution and documenting the payment disbursement process, including distribution of ID cards, collection of required documents, preparing the micro Plan and confirmation taken from the affected persons. Up to this reporting period, no impact on common property resources (CPRs) in the working areas has been reported.

Grievance Redress Mechanism (GRM) has been established under this sub-project. PIUs, with support from the Construction Management Supervision Consultant(CMSC) & contractors, are responsible for maintaining a proper grievance register and ensuring that the grievances received during execution are recorded and resolved within the specified timeframe. The contractor also shared toll-free numbers with the households and local public through their social outreach team for lodging complaints/grievances, if any, during the execution of works. During the reporting period, minor complaints from the people

(housekeeping, pipeline damage, leakages in a new connection, etc.) were received, which have been resolved satisfactorily.

A series of meetings and consultations were held with the affected persons and other stakeholders regarding the scope of the project, entitlement options, impacts etc. at different stretches during resettlement plan preparation and implementation. Leaflets with information about the subproject, its benefits, and grievance redress mechanism were also distributed to the households. Key findings of consultations are: (i) participants expressed satisfaction that there was a subproject taking care of their needs, which they have waited for 25-30 years; (ii) they raised that it is important to cover up the dug pit and trenches properly and restore the roads after sub-project construction.

The Safeguard Specialist- Resettlement of PMCBC and Social Safeguard and Gender Professional of both CMSCs are monitoring the overall social safeguards activities and coordination among the PMU, PIUs, CMSC, contractors and local people. The consultant visited sites during this reporting period in order to investigate possible involuntary resettlement impacts, implementation of resettlement plan and related social safeguards issues. The Safeguard Specialist- Resettlement of PMCBC provided training/Sensitized to PIUs'/CMSC and Contractor engineers on ADB's policies and guidelines.

A. PROJECT BACKGROUND AND DESCRIPTION

1. The Rajasthan Secondary Towns Development Sector Project (RSTDSP), is the fourth phase of investment projects financed by Asian Development Bank (ADB) and implemented by the Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited-Externally Aided Projects (RUDSICO-EAP), previously known as Rajasthan Urban Infrastructure Development Project (RUIDP). RSTDSP aims to improve water supply sewerage and other infrastructure services in secondary towns of Rajasthan with populations ranging from 20,000-115,000 through a sector loan modality. The project is aligned with the following impact(s): (i) improvement in access to potable, affordable, reliable, equitable, and environmentally sustainable drinking water supply in all urban areas of Rajasthan (ii) improvement in health status of urban population, especially the poor and under-privileged through improvements in sewerage systems of sub-project towns (iii) improvements in other infrastructure services of some towns. Under RSTDSP, work is in progress in 14 project towns. From the savings under the ongoing project of RSTDSP, the Government of Rajasthan (GoR) has decided to implement Faecal Sludge and Septage Management (FSSM) through the construction of FSTPs in selected 13 towns that do not have a central sewer network. The project is expected to increase operational efficiency, improve service delivery, and positively impact health and quality of life for the residents of project towns in the State.

2. Project Components: The project includes interventions in 14 towns: Abu Road, Banswara, Didwana, Fatehpur, Khetri, Kuchaman, Ladnu, Laxmangarh, Makrana, Mandawa, Pratapgarh, Ratangarh, Sardarshahar, and Sirohi. Water supply subprojects are included in 8 towns and sanitation in 13 towns (Table 1 and Figure 1). The project is financing infrastructural development, in the form of construction and rehabilitation, related to water supply and wastewater inclusive of capacity building of existing Municipal bodies. The works proposed for 14 selected towns are depicted in Table 1(A).

3. From the savings under the RSTDSP Project, the Government of Rajasthan (GoR) has decided to implement Faecal Sludge and Septage Management (FSSM) through the construction of FSTPs in selected 13 towns⁷ that do not have a central sewer network. The project is expected to increase operational efficiency, improve service delivery, and positively impact health and quality of life for the residents of project towns in the State.

4. Impact of the project, RSTDSP: The water supply improvements are expected to benefit all, including the urban poor, by reducing water collection time from other sources, which may be costly or unhygienic; and by minimizing earning losses from missed work due to waterborne diseases. The project also aims for wastewater reuse and a city-wide, inclusive sanitation approach to improve sanitation for all, including below poverty line households. Social and

⁷ Bari (Dholpur), Deeg (Bharatpur), Pilibanga (Hanumangarh), Suratgarh (Sri Ganganagar), Shahpura (Bhilwara), Bhinder-Kanod (Udaipur), Gangapur (Bhilwara), Bhawani Mandi (Jhalawar), Dausa, Tijara (Alwar), Bandikui (Dausa), Jobner (Jaipur) Neem Ka Thana (Sikar) and Shahpura (Jaipur).

community development is an important component of the project, involving community mobilization under well-organized proactive public awareness campaigns.

Table 1: Summary of Proposed Improvements in Project Towns.

Subprojects	ULBs
Water supply (8 ULBs)	Abu Road, Banswara, Khetri, Kuchaman, Laxmangarh**, Mandawa, Sardasahar, Sirohi
Sanitation (13 ULBs)	Abu Road, Banswara, Didwana, Fatehpur*, Khetri, Kuchaman, Ladnu, Mandawa, Makrana*, Pratapgarh*, Ratangarh*, Sardasahar, Sirohi
FSSM-(13 ULBs)	Bari (Dholpur), Deeg (Bharatpur), Pilibanga (Hanumangarh), Suratgarh (Sri Ganganagar), Shahpura (Bhilwara), Bhinder-Kanod (Udaipur), Gangapur (Bhilwara), Bhawani Mandi (Jhalawar), Dausa, Tijara (Alwar), Bandikui (Dausa), Jobner(Jaipur) Neem Ka Thana (Sikar) and Shahpura (Jaipur).

* Indicates that the project is only investing in sanitation in that ULB, and not water supply.

** Indicates that the project is only investing in water supply in that ULB, and not sanitation.

Source: Monthly Progress Report (MPR) September- 2024

Figure 1: Location of project towns-RSTDSP



Table 1(A): Description of the subprojects

S.no	Name of the Town	Type of work	Package Number	Description of the project	Approved SIP Amount with O&M (Cr. Rs.)
1	Abu Road	W/S	RSTDIP/ABR/01	Construction of works of water supply production and distribution network improvement with house service connections for nonrevenue water reduction and continuous water supply and providing sewer network with house connections and construction of sewage treatment plant and all allied works and operation services of the entire system for 10 years at Abu-road town	269.99
		W/W			
2	Sirohi	W/S	Lot 1- RSTDIP/SHR/01	Construction of works of water supply production and distribution network improvement with house service connections for nonrevenue water reduction and continuous water supply and providing sewer network with house connections and construction of sewage treatment plant and all allied works and operation services of the entire system for 10 years at Sirohi town	213.99
		W/W			
3	Sardarshar	W/S	RSTDIP/SRD/01	Design and construction of works of water supply and providing sewer network with house sewer connections along with construction of sewage treatment plant & sewerage pumping station and all allied works and operation services of the entire system for 10 years at Sardarshahar (Churu)	194.45
		W/W			
4	Banswara	W/S	RSTDIP/BNS/02	Construction of works of water supply production and distribution network improvements with house service connections for nonrevenue water reduction and continuous water supply and providing sewer network with house sewer connections, along with construction of sewage treatment plant & sewerage pumping station and all allied works and operation services of the entire system for 10 years at Banswara town	319.92
		W/W			
5	Khetri	W/S	RSTDIP/KTR/03	Construction of works of water supply production and distribution network improvements with house service connections for nonrevenue water reduction and continuous water supply and providing sewer network with house sewer connections, and construction of sewage treatment plant and all allied works and operation services of the entire system for 10 years at	77.36
		W/W			

S.no	Name of the Town	Type of work	Package Number	Description of the project	Approved SIP Amount with O&M (Cr. Rs.)
				Khetri (Jhunjhunu)	
6	Kuchaman	W/S	RSTDIP/KMN/02	Construction of works of water supply production and distribution network improvements with house service connections for nonrevenue water reduction and continuous water supply and providing sewer network with house connections, and construction of sewage treatment plant & sewage pumping station and all allied works and operation services of the entire system for 10 years at Kuchaman (Nagaur)	314.9
		W/W			
7	Mandawa	W/S	RSTDIP/MDW/03	Construction of works of water supply production and distribution network improvements with house service connections for nonrevenue water reduction and continuous water supply and providing sewer network with house sewer connections, and construction of sewage treatment plant, sewerage pumping station and all allied works and operation services of the entire system for 10 years at Mandawa (Jhunjhunu)	106.45
		W/W			
8	Ratangarh	W/W	RSTDIP/RTG-FTP-LXG/01-Lot 01	Construction of Sewer network with house connections, and construction of sewage treatment plant & sewage pumping station and all allied works and operation services of the system for 10 years at Ratangarh (Churu)	179.12
9	Fatehpur	W/W	RSTDIP/RTG-FTP-LXG/01-Lot 02	Construction of works of Sewer network with house connections, and construction of sewage treatment plant & sewage pumping station and all allied works and operation services of the system for 10 years at Fatehpur (Sikar)	104.35
10	Laxmangarh	W/S	RSTDIP/RTG-FTP-LXG/01-Lot 03	Construction of works of water supply distribution network improvements with house service connections for nonrevenue water reduction and continuous pressurized water supply and operation services of the entire system for 10 years at Laxmangarh (Sikar)	49.52
11	Pratapgarh	W/W	RSTDIP/PRT/01	Construction of Sewer system including sewerage network, sewage treatment plant, sewage pumping station and house sewer connection along with all allied works and operation services of the entire system for 10 years at	181.18

S.no	Name of the Town	Type of work	Package Number	Description of the project	Approved SIP Amount with O&M (Cr. Rs.)
				Pratapgarh	
12	Ladnu	W/W	RSTDIP/LDN-DID-MKN/01-Lot 01 (Lot 2-RSTDIP/LDN/01)	Construction of works of Sewer network with house connections, and construction of sewage treatment plant and all allied works and operation services of the entire system for 10 years at Ladnu (Nagaur)	174.55
13	Didwana	W/W	RSTDIP/LDN-DID-MKN/01-Lot 02 (Lot 2-RSTDIP/DID/01)	Construction of works of Sewer network with house connections, and construction of sewage treatment plant & sewage pumping station and allied works and operation services of the entire system for 10 years at Didwana (Nagaur)	79.4
14	Makrana	W/W	RSTDIP/LDN-DID-MKN/01-Lot 03 (Lot 2-RSTDIP/MKN/01)	Construction of works of Sewer network with house connections, and construction of sewage treatment plant & sewage pumping station and allied works and operation services of the entire system for 10 years at Makrana (Nagaur)	131.53

Source: Monthly Progress Report (MPR) March- 2025

B. PURPOSE OF THE REPORT

5. The purpose of the semiannual social safeguard monitoring report (SSMR) is to analyze periodically over the total implementation period of the project to comply with the approved involuntary resettlement (IR) documents such as resettlement plans (RP)/ Resettlement and Indigenous Peoples Plans(RIPPs) and due diligence reports (DDR). RSTDSP has the responsibility to oversee the implementation and monitoring of social safeguards issues of each subproject in the project towns. This report covers resettlement and social safeguard monitoring results to comply with the spirit of ADB policy to 'enhance stakeholders trust' and ability to engage with ADB, and thereby increase the development impact (of projects) in which disclosure of safeguard monitoring is a prominent aspect. This report covers social monitoring, addressing all the issues related to social safeguards, with reference to the progress achieved and the current status of the reporting period. The PMU is scheduled to provide the monitoring report on social safeguards activities at semiannual basis. The current report is the 8th Semiannual Social Safeguard Monitoring Report (SSMR) prepared for the reporting period from **October 2024 to March 2025**, in accordance with the ADB Safeguard Policy (SPS), 2009.

C. SOCIAL SAFEGUARD CATEGORIZATION

6. The construction of the sub-projects does not require any acquisition of land or cause permanent displacement except for Fatehpur and Makrana town, where a small portion of private lands for sewage pumping stations (SPS) has been purchased by Municipality through negotiated settlement and updated resettlement documents has been submitted to ADB. At

Kuchaman water supply and wastewater subproject, the proposed land (425 sq meter) for SPS 3.1 MLD has been obtained under exchange of land parcel. Due diligence has been done and has been reported to ADB by updated RP and previous SSMR. The locations for the permanent site (sewerage treatment plants, water treatment plants (WTP), sewerage pumping stations (SPS), Consumer Relation Management Centers (CRMC), Central Control Center (CCC) etc.) have been carefully selected and proposed in the vacant encumbrance free government land while the pipelines for water supply and sewerage are being laid within road rights-of-way (RoW). The main resettlement impact is the potential reduction in the income of vendors/hawkers operating in the right of way(RoW). During laying pipelines, the presence of trenches, excavated soil, and machinery make it difficult for customers to reach at that location where of vendors/hawkers are operating their petty businesses.

7. Screening and impact assessment was done by the team of detailed project report (DPR) consultants, safeguard consultant, and staff from ULBs in all the 13 towns, where FSSM works are proposed from saving under the project and it was confirmed that all the proposed works have no involuntary resettlement impacts. For location change of FSTPs at Bari, Deeg, Shahpura (Jaipur) & Pilibanga-Suratgarh, updated Due Diligence Reports were prepared as per SPS 2009 and same has been approved by ADB. During this reporting period all the DDRs of FSTPs have been updated and approved by the ADB.

8. As impacts are not significant, hence the sub-projects under Loan 3972-IND has been categorized as 'B' for involuntary resettlement (IR) and 'B⁸' for Indigenous People (IP) in accordance with the ADB's SPS 2009, which applies to this project.

9. Impacts on Indigenous Peoples: Three subprojects Abu Road, Pratapgarh and Banswara are declared as a scheduled area by the Government of India. Whilst many Scheduled Tribe (ST) households residing in these three town; no longer maintain their cultural traditions and have settled amongst the non-tribal populations. The project is designed to benefit 100% scheduled tribe households in the project coverage area. House service connections for sewerage are included in project costs. Further, to address any potential safeguards issues and ensure maximum benefits reach the scheduled tribe households, a specific action plan for indigenous peoples is proposed for this subproject. The action plan includes the following specific activities: (i) a baseline survey⁹ has been conducted for identification and inclusion of indigenous peoples households within the project coverage area; (ii) proposed benefits (e.g.) to indigenous peoples households are being shared and monitored; (iii) IEC materials, information sharing, consultations and other activities¹⁰ stated in the CAPP are being made culturally sensitive and appropriate when implemented in the scheduled area;

⁸ Abu Road, Pratapgarh and Banswara) has been declared as a scheduled area by the Government of India.

⁹ Contractors will conduct connection campaigns across the project coverage area and will be responsible to ensure that IP households and localities are identified and included in the campaign. Data on exact number of scheduled tribe households can be generated from the house service connection survey (pertaining to both water supply and wastewater/sewerage) to be conducted by the project contractor prior to start of civil work. The localities where sewerage network will not laid shall be covered through FSM. Cost for such activity is already included in the contract document for the subproject.

¹⁰ CAPP will be primarily responsible for planning implementing and monitoring the result of such activities.

(iv) In case of any indigenous peoples impacts in the sub-project, the chief of the tribe or a member of the tribal council (to ensure that traditional grievance redressal systems are integrated) and an NGO working with Indigenous peoples will be involved as traditional arbitrator. GRC is also ensuring that grievance redress established is gender inclusive in receiving and facilitating the resolution of the Indigenous Peoples (IPs') concerns; (v) consultations with Indigenous Peoples (IPs) households are being conducted in all subproject stages which shall help in identifying any culture-specific requirements and traditions like avoidance of any specific festival days, and/or other activities with cultural significance to the Indigenous Peoples communities during civil work; and any other Indigenous Peoples related issues and concerns that may be of importance to the community. An end-line sample survey¹¹ will be conducted to document the views of Indigenous Peoples households about subproject benefits. Such a survey is in line with subproject internal monitoring.

D. STATUS OF PREPARATION/ UPDATING OF RPs/RIPPs

10. Draft resettlement plans (RPs) for eight subprojects¹² and draft Resettlement and Indigenous Peoples Plans (RIPPs) for three subproject¹³ were prepared for the 11 selected project cities/towns during the loan processing stage. Three subprojects¹⁴, where no involuntary resettlement(IR) impacts were envisaged during the initial assessment, due diligence reports were prepared as per SPS, 2009. (Details of social safeguard documents are provided in Table 2) All the RPs/RIPPs have been revised based on a detailed measurement survey (DMS), approved design and alignment, 100% census & socio-economic survey of potential affected persons during implementation by Construction Management Supervision Consultant (CMSC) in line with the resettlement framework of RSTDSP. During the implementation of the subproject in Fatehpur and Makrana town, urban local bodies of both towns purchased a small portion of private land (through negotiated settlements) as government land was not available in the particular locations where the design was prepared. Due diligence has been done by safeguard professional and third party validation has also been done. The updated due diligence report of the Fatehpur and Makrana waste water subproject has been submitted to ADB for approval and has also been reported to ADB through SSMR. By the end of this reporting period disbursement of resettlement assistance has been completed in Abu Road, Sirohi, Ratangarh, Laxmangarh, Sardarshahar, Pratapgarh, Banswara, Mandawa, Khetri, and Ladnu. Resettlement assistance of 15 potential affected persons is pending in Kuchaman only due to pending of pipe laying work in APs area.

11. **Status of Revised DDRs of 13 FSTP towns:** Under the Faecal Sludge and Septage Management (FSSM), construction of FSTPs with different capacities was proposed in 13 towns that do not have a central sewer network. In all the towns, FSTP is proposed in the government vacant land; hence, no involuntary resettlement impacts were envisaged. DDRs for all 13 towns were prepared and approved by ADB. FSTP location has been changed in 04

¹¹ Cost towards conducting end-line sample survey is included in the subproject budget table. Sample size may be decided by the Project in consultation with ADB.

¹² Sirohi, Sardarsahar, Laxmangarh, Ratangarh, Khetri, Mandawa, Kuchaman, Ladnu.

¹³ Abu Road, Pratapgarh and Banswara.

¹⁴ Fatehpur, Makrana and Didwana

project towns i.e. Deeg, Bari, Shahpura, and Pilibanga-Suratgarh, and DDRs of all 04 towns have been submitted and approved by ADB. Additionally, the DDRs of the remaining 09 towns, Shahpura (Bhilwara), Bhinder-Kanod (Udaipur), Gangapur (Bhilwara), Bhawani Mandi (Jhalawar), Dausa, Tijara (Alwar), Bandikui (Dausa), Jobner (Jaipur) Neem Ka Thana (Sikar) and Shahpura (Jaipur) has also been updated based on the final design/ drawings and updated public consultations, and all 09 updated DDRs have been submitted and approved from ADB.

12. CC approach road (560 meters in length) to STP Pratapgarh has been constructed, which was not an item of BoQ. Social safeguard due diligence has been carried out during this reporting period to assess the IR and IP impact due to the construction of CC road on the existing road. No IR impact was envisaged nor it causes any risks to indigenous people in accordance with ADB SPS. The whole process will be discussed in the final RP of Pratapgarh waste water subproject and will be submitted to ADB for approval.

13. Being a Design-Build Operate (DBO) contract, even though consultants prepare the detailed project reports (DPRs), the final design/alignment was to be provided/ re-confirmed by the contractor. While preparing revised RPs/RIPPs, the vendors on both sides of the road were considered affected persons (APs) to avoid complications. Further, to facilitate RPs/RIPPs implementation, a list of affected persons identified during the Social Impact Assessment (SIA) with 100% socio-economic details was provided to contractors for freezing of alignment and for avoiding/ confirming the impacts on affected persons.

Table 2: Details of Social Safeguard Documents

S.N.	Package number	Name of Town and type of projects	Type of Documents	Categorization
1.	RSTDIP/RTG-FTP-LXG/01	Ratangarh Sewerage	RP	B
2.		Fatehpur Sewerage	DDR	C
3.		Laxamangarh Water Supply	RP	B
4.	RSTDIP/SRD/01	Sardarshahar Water Supply and Sewerage	RP	B
5.	RSTDIP/SHR-ABR/01	Abu Road Water Supply and Sewerage	RIPP	B
6.		Sirohi Water Supply and Sewerage	RP	B
7.	RSTDIP/PRT/01	Pratapgarh Sewerage	RIPP	B
8.	RSTDIP/BNS/04	Banswara Water Supply and Sewerage	RIPP	B
9.	RSTDIP/KTR/03	Khetri Water Supply and Sewerage	RP	B
10.	RSTDIP/LDN-DID-MKN/01	Ladnu Sewerage	RP	B
11.		Didwana Sewerage	DDR	C
12.		Makrana Sewerage	DDR	C
13.	RSTDIP/KMN/02	Kuchaman Water Supply and Sewerage	RP	B
14.	RSTDIP/MDW/03	Mandawa Water Supply and Sewerage	RP	B

Source: Data received from CMSC-I & II, and compiled by PMCBC

E. IMPLEMENTATION OF THE RESETTLEMENT PLAN

14. The methodology followed for implementing RPs/RIPPs is as follows: Before the start of work; contractors provide the advance work plan to PIU & CMSC along with the final alignment.

After the intimation by the contractor, the joint re-confirmatory survey is conducted by the officials of PIU, CMSC, and the contractor to finalize the list of affected persons likely to be impacted due to civil works. Since the exact alignment was not known when preparing draft RPs/RIPPs, the RPs/RIPPs contained the details of all the business establishments likely to be impacted. While finalizing the alignment, efforts are made to avoid the impacts, and accordingly, the affected persons present in the section are included in the mitigation list.

15. The area where the mitigation of impacts on livelihood will not be possible, all the affected persons will be re-validated/ verified by the implementing officer / Safeguard Support Staff of CMSC, and identity card(ID) cards will be disbursed to potential affected persons. During the re-validation, If the affected persons listed in the RPs/RIPPs are not available at the site during all the phases (i) Re-verification, (ii) distribution of compensation, and (iii) construction phase, they will be treated as “missing,” and confirmation of their absence is being obtained from the other affected households(AHs). If affected persons are voluntarily inclined not to receive the compensation despite being offered, they will be treated as “Unwilling,” and their consent will be given in writing.

16. Once the list is finalized, Safeguard Support Staff collects the details required from affected persons, which include the bank details and other necessary documentation required for the transfer of compensation. Based on the findings, the micro plans will be prepared, and after approval/sanction by PIU, these micro plans will be submitted to the treasury with the required bank details for direct transfer of the compensation in the bank account of affected persons through electronic clearance service/National Electronic Fund Transfer (NEFT) payment.

17. Affected persons are being compensated in accordance with the agreed entitlement matrix of RF. Affected persons are being compensated for 14 days' disturbance as per the resettlement framework (RF); however, micro plans prepared for the project area take care of the real impacts on affected persons, and it is ensured that all the affected persons are compensated for the actual period of disturbance. If the duration of impact is more, they will be compensated for the actual period of disturbance after due verification from PIU. The compensation that will be recommended in the micro Plan, will considered the entitlements prescribed in the resettlement plan (livelihood assistance, shifting assistance, and vulnerability assistance), the time lags (7% inflation in survey income is provided per year) of implementation & survey along with additional compensation with respect to minimum wage rates.

F. CURRENT STATUS OF RP – IMPLEMENTATION

18. Contracts for all 14 towns have been awarded, and pipe laying work for wastewater and water supply networks has progressed considerably in all the towns. The physical progress along with details of the contractor of the subprojects, are provided in **Appendix 1**. As per survey data of 11 towns, where RPs and RIPP were prepared, total of **3221** potential affected persons (Abu Road-435, Sirohi-349, Sardarsahar-412, Ratangarh-287, Laxmangarh-201,

Pratapgarh-412, Banswara-391, Mandawa-77, Khetri-42, Ladnu-252, and Kuchaman-363) was identified, among **1286** comes under vulnerable category¹⁵. A summary of the potentially affected person's subproject wise is presented in Table 3.

Table 3: No. of APs reported as per socio-economic survey

Name of Town	Sub -project Name	Type of Impact	No. of APs	No. of Vulnerable APs
Abu Road	Water supply and Waste Water	Temporary	435	245
Sirohi	Water supply and Waste Water	Temporary	349	154
Ratangarh	Waste Water	Temporary	287	76
Laxmangarh	Water Supply	Temporary	201	61
Sardarsahar	Water supply and Waste Water	Temporary	412	157
Pratapgarh	Waste Water	Temporary	412	148
Banswara	Water supply and Waste Water	Temporary	391	263
Mandawa	Water supply and Waste Water	Temporary	77	21
Khetri	Water supply and Waste Water	Temporary	42	4
Ladnu	Waste Water	Temporary	252	56
Kuchaman	Water supply and Waste Water	Temporary	363	101
Total			3221	1286

Source: Data received from CMSC-I & II, and compiled by PMCBC

19. Pipelines of sewer and water supply network have already been started in all towns. By the end of the reporting period, the resettlement assistance of ₹ **1,94,21,284** has been paid to **2033** numbers affected persons, while 41 affected persons have shown their unwillingness (voluntarily inclined not to receive compensation), and 708 affected persons are under the missing category (which were not available at the site at the time of construction) and impact avoided for 424 affected persons (Details are provided in Table 4 to 5). Resettlement assistance has been provided to 5 APs in Kuchaman towns during this reporting period (October 2024 – March 2025). The compensation was paid to affected persons as per the approved micro Plan, which includes livelihood assistance, shifting assistance, vulnerability assistance, and additional assistance (for the time lag to maintain the minimum wage level. Records of written information from surrounding vendors or shopkeepers have been collected for missing (those not available at the site during execution of work) and unwilling affected persons. The project implementation unit has all the details of the persons who are missing and voluntarily not inclined or unwilling to be affected. Details of compensation disbursed during this reporting period are attached in **Appendix 2**, and the photographs of identity card distribution to affected persons are attached in **Appendix 3**.

¹⁵ Vulnerable households comprise below poverty line households, female-headed households, households with out of school/working children, disabled person-headed household, elderly headed household, landless household, household with no legal title/tenure security, and schedule caste and scheduled tribe households.

Table 4: Number of affected persons Paid assistance

Town	No. of APs	Status of Payment disbursement		Status of APs		
		APs Paid (up to September 2024)	APs Paid (up to March 2025)	Unwilling APs (up to March 2025)	Nos of APs Missing (up to March 2025)	Impact Avoided/mitigated (up to March 2025)
Abu Road	435	306	306	1	128	0
Sirohi	349	265	269	0	80	0
Ratangarh	287	123	123	1	111	52
Laxmangarh	201	98	98	17	29	57
Sardarsahar	412	166	166	7	89	150
Pratapgarh	412	219	219	3	62	128
Banswara	391	290	290	0	74	27
Mandawa	77	57	57	2	18	0
Khetri	42	32	32	0	10	0
Ladnu	252	126	195	5	42	10
Kuchaman	363	147	278	5	65	0
	3221	1829	2033	41	708	424

Source: Data received from CMSC-I & II, and compiled by PMCBC

Table 5: Status of payment to affected persons

Town	Total APs	Total Assistance Disbursed till March 2025		Type of Assistance Disbursed to APs (Till March 2025)					
				Livelihood Assistance		Shifting Assistance		Vulnerability Assistance	
		APs	Amt	APs	Amt	APs	Amt	APs	Amt
Abu Road	435	306	3519738	306	1305738	306	459000	195	1755000
Sirohi	349	269	2754084	269	1270584	269	403500	120	1080000
Ratangarh	287	123	999702	123	566202	55	82500	39	351000
Laxmangarh	201	98	795710	98	486710	98	147000	18	162000
Sardarsahar	412	166	1297598	166	703598	144	216000	42	378000
Pratapgarh	412	219	1850538	219	892038	219	328500	70	630000
Banswara	391	290	3209814	290	1136814	290	435000	182	1638000
Mandawa	77	57	594000	57	346,500	57	85500	18	162000
Khetri	42	32	275100	32	191100	32	48000	4	36000
Ladnu	252	195	1540600	195	933100	195	292500	35	3,15,000
Kuchaman	363	278	2584400	278	1303400	278	417000	96	864000
Total	3221	2033	19421284	2033	9135784	1943	2914500	819	7371000

Source: Data received from CMSC-I & II, and compiled by PMCBC

Project Impacts Minimization

20. Meticulous planning by PIU and project consultant and good practices adopted by the contractor have resulted in mitigation of impact on affected persons. The good practices adopted by the contractor are as below (including but not limited to following): -

- Sewer pipelines were laid in the middle of the road, and works were executed in night with proper safety measures.
- Worked was executed on one segment at the time on one side of the road, and access was made available for the roadside petty businesses. Excavation has been expedited, and walkways have been provided for access in order to avoid livelihood losses.

21. During the preparation of the resettlement plans, the people carrying out business activities on both sides of the road were considered affected persons. During implementation, works are being executed in some areas (high density) at night time or through a trenchless method, and access was ensured to affected persons in a few patches. Accordingly, no impact was sustained by vendors operating. All these affected persons have been considered as mitigated and reported in the SSMR.

22. Up to this reporting period, impacts on 424 affected persons (150 in Sardarshahar, 128 in Pratapgarh, 52 in Ratangarh, 27 in Banswara, 57 in Laxmangarh & 10 in Ladnu) were avoided/ mitigated as work was executed on one segment at the time on one side of the road, or work was executed in night time, and access was made available for the roadside petty businesses. Assistant Safeguard staff posted in towns are conducting regular due diligence of work execution and documenting the confirmation taken from the mitigated affected persons. No impact mitigation was done during this reporting period. (Table 6).

Table 6: Details of affected persons mitigated up to March 2025

Town	Package no	No. of APs	Impact Avoided (up to this reporting period)	Remarks
Sardarsahar	RSTDIP/SRD/01	412	150	Works were executed in some areas (Bus Stand) at night time; hence, impacts of potential affected persons was totally avoided. This has been reported to ADB in previous SMR.
Laxmangarh	RSTDIP/LXG/01	201	57	Works were executed in one side of the road, hence no livelihood impacts were envisaged on potential affected persons running their business on other side of the roads. This has been reported to ADB in previous SMR.
Pratapgarh	RSTDIP/PRT/01	412	128	Works were executed in some areas (high density) in night time, hence impacts of potential affected persons was totally avoided. This was reported to ADB in a previous SMR.
Ratangarh	RSTDIP/RTG/01	287	52	Works were executed on one side of the road; hence, no livelihood impacts were envisaged on potential affected persons running their businesses on the other side of

Town	Package no	No. of APs	Impact Avoided (up to this reporting period)	Remarks
				the roads. This was reported to ADB in the previous SMR.
Banswara	RSTDIP/BNS/04	391	27	Works were executed on one side of the road; hence, no livelihood impacts were envisaged on potential affected persons running their business on the other side of the roads.
Ladnu	RSTDIP/LDN/01	252	10	Works were executed on one side of the road; hence, no livelihood impacts were envisaged on potential affected persons running their business on other side of the roads.
Total			424	

Source: Data received from CMSC-I & II, and compiled by PMCBC

23. **Impacts on Indigenous People:** Based on the census and socio-economic survey of Abu Road, Pratapgarh, and Banswara, declared as scheduled areas by the Government of India, the likely affected persons facing involuntary resettlement impact (temporary income loss) were 41 in Abu Road, 20 in Pratapgarh and 175 in Banswara from the Scheduled Tribe community. These people were using the RoW for earning their livelihood by selling fruits, garments, flowers etc. and were likely to be affected from work for a temporary period of work. During freezing of final alignment, efforts were made by the implementing agency to provide access for continuation for their livelihood. Wherever temporary livelihoods impacts were persisted during the execution of work, additional compensation and assistance was distributed to them as per the agreed resettlement framework and planning framework of the indigenous people. In order to mitigate negative impacts on scheduled tribe persons, before and during the subproject design, implementation, as well as monitoring process, the project staff is disseminating the project information and conducting meaningful consultation especially with scheduled tribe persons to ensure that they get the maximum benefit from the advantage conditions brought by the subproject and fully understand their entitlements under this RIPP. No civil works were allowed in sections of impact and compensation payment has completed prior to start of civil works.

24. In compliance to the action plan, consumer survey has been completed in Abu Road, Pratapgarh and Banswara town. (ward wise details of scheduled tribe in Abu Road, Pratapgarh and Banswara town is presented in **Appendix 4**. Several round of consultation done with scheduled tribe households in these towns and project scope and advantages was disseminated to them. It was conveyed that 100% house service connections for sewerage and potable water will be provided to scheduled tribe households. CAPP consultants are developing IEC materials, and will be provide skill training, formation of groups, linkage with livelihood scheme etc.

G. CURRENT STATUS OF FSSM – IMPLEMENTATION

25. Under the project, from the savings amount, the Government of Rajasthan (GoR) has decided to implement Faecal Sludge and Septage Management (FSSM) through the construction of FSTPs in selected 13 towns, that do not have a central sewer network. Name of towns and their current status is provided in Table below. The project is expected to increase operational efficiency, improve service delivery, and positively impact health and quality of life for the residents of project towns in the State. In all the towns, FSTP is proposed in the government vacant land, hence no involuntary resettlement impacts were envisaged. DDRs were prepared for all the towns and get approved from ADB. Contract of all the towns have been awarded and excavation and construction works have also been progressed considerably. FSTP location has been changed in following four towns (Deeg, Bari, Shahpura (Jaipur) & Pilibanga-Suratgarh). Due diligence has been done and DDRs of all four towns have also been updated and submitted to ADB and get approval accordingly. the DDRs of remaining 09 towns, Shahpura (Bhilwara), Bhinder-Kanod (Udaipur), Gangapur (Bhilwara), Bhawani Mandi (Jhalawar), Dausa, Tijara (Alwar), Bandikui (Dausa), Jobner (Jaipur) Neem Ka Thana (Sikar) and Shahpura (Jaipur) has also been updated based on the final design/ drawings and updated public consultations, and all 09 updated DDRs have been submitted and approved from ADB. Contracts for all the 14 towns have been awarded and pipe laying work for waste water and water supply networks has been progressed considerably in all the towns. Construction of FSTPs are also being carried out at a fast pace, except in Shahpura (Jaipur) due to public protest against new land allotment, work could not be started till the end of this reporting period. Photographs of civil work under FSSM towns are attached in **Appendix 5** and details of consultation with stakeholders & community are attached in **Appendix 6**.

Status of FSSM sub-projects

S.no	Town	Sub-project Name	Type of Documents	Document Status
1	Bandikui	FSSM	DDR	Approved
2	Bari	FSSM	DDR	Approved
3	Dausa	FSSM	DDR	Approved
4	Deeg	FSSM	DDR	Approved
5	Kanode- Bhinder	FSSM	DDR	Approved
6	Neem Ka Thana	FSSM	DDR	Approved
7	Shahpura	FSSM	DDR	Approved
8	Tijara	FSSM	DDR	Approved
9	Bhawani Mandi	FSSM	DDR	Approved

S.no	Town	Sub-project Name	Type of Documents	Document Status
10	Jobner	FSSM	DDR	Approved
11	Pilibanga-Suratgarh	FSSM	DDR	Approved
12	Gangapur	FSSM	DDR	Approved
13	Shahpura	FSSM	DDR	Approved

Source: Data shared by CMSC-I & II, and compiled by PMCBC

H. PUBLIC PARTICIPATION AND CONSULTATION

26. A series of meetings and consultations were held with the potential APs and other stakeholders regarding the scope of the project, entitlement options, impacts etc. at different stretches during RPs/RIPPs preparation. Key findings of consultations are: (i) participants expressed satisfaction that there was a subproject taking care of their needs which they have waited for 25-30 years; (ii) they are not hesitant to move or shift if necessary to accommodate the work; (iii) they are willing to provide labor for the subproject; and (iv) they raised that during pipe laying works proper barricading should be done at site and it will be required to cover up the dug holes properly and restore the roads after sub-project construction. Prior to start of inventory loss survey, leaflet with information about the subproject, its benefits, grievance redress mechanism were also distributed to the potential affected persons as well as households.

27. Door to door consultation with public was held and importance of water metering, property connection, Water conservation and issues related to sewerage connectivity was discussed and need for their support was conversed. Advance intimation about works plan was conveyed to households.

28. The consultation was held very close to the area where work is ongoing and was attended by people in the surrounding areas. No consultation with ST community people in Pratapgarh, Banswara, and Abu Road was organized during this reporting period as RP implementation was completed and CMSC support staff demobilized. Social support staff, the Social outreach team, and representatives from contractors also participated in the events and interacted with the people. A summary of consultation done in each project town during this reporting period is presented in **Table 7**. Consultation with stakeholders & community (Photograph & Sample consultation sheet) are attached in **Appendix 6**.

29. People are very willing to extend their cooperation as the project will provide much-needed potable water and sewerage facilities. It was conveyed that some relatively adverse issues such as water supply quantity and quality, will be hampered during physical work once the civil work will be started. It was also deliberated with the households that temporary access issues may arise during the laying of the pipeline, although mitigation measures will be taken by contractors as per site-specific Environmental Monitoring Plan (EMP).

Table 7: Summary of Consultations with stakeholders & public in Project Towns during this reporting period

S.no	Town	Consultations	Male	Female	Total Participation
1	Consultation with Schedule Tribes	0	0	0	0
2	Abu-road	3	5	7	12
3	Ratangarh	0	0	0	0
4	Sirohi	0	0	0	0
5	Sardarshar	1	36	0	36
6	Laxmangarh	0	0	0	0
7	Fatehpur	0	0	0	0
8	Pratapgarh	0	0	0	0
9	Banswara	0	0	0	0
10	Khetri	54	395	159	554
11	Kuchaman	98	853	901	1754
12	Ladnu	54	237	162	399
13	Mandawa	178	1111	993	2104
14	Didwana	11	69	16	85
15	Makrana	41	340	120	460
	Total	440	3046	2358	5404

Source: Data shared by CMSC-I & II, and compiled by PMCBC

30. M/s IPE Global Pvt Ltd has been appointed as Community Awareness and Public Participation Consultants (CAPPC) to oversee the entire information dissemination required for creating public awareness. The Social Development Expert of CAPP along with town level staff of CAPPC with the support of the social outreach team (SOT)¹⁶ of the contractor is implementing awareness program in the project towns. The major activities that are performed by CAPPC are: develop awareness material targeting different sections of society, promote gender equality and social inclusion through water and sewer connection to BPL, empowerment of schedule caste/schedule tribe households, capacity building and training for ULB staff and public representatives, mobilize the community with regular field-level activities involving all stakeholders, keep a stock of Quantitative achievements and targets achieved, collect feedback from all stakeholders within the town.

31. During this reporting period, CAPPC has organised extensive awareness activities involving residents, public representatives, shopkeepers, women, project labours, line departments and school children. Development of communication and IEC material for successfully delivering a key message. Capacity building of Social Outreach Team from contractors, public representatives and ULB staff members was conducted in towns.

32. Activities with Schools & Households for water audits were organized in secondary & Additional Financing towns. Focused group discussions with women and women Elected representatives of the concerned towns were organised.

¹⁶ Dedicated SOT teams will be mobilized by contractor for facilitating the CAPPC activities (including R&R activities). CAPPC is regularly evaluating the performance of the contractors Social Outreach Teams.

33. Concerning the GESI action plan, a Total no of 30 trainings were organized on Plumber, Basic Computer and Mason in WSS project towns. The duration of Plumbing & Mason skill training is two weeks and Basic computer skill training is four weeks in the respective towns. Total number of women trained is 194 out of which 43 belongs to scheduled caste, 39 belongs to Scheduled Tribe, 89 belongs to OBC and 23 belongs to General Caste categories. Photographs of women internship program and skill training and news coverage of concerned activities are appended in **Appendix- 7**.

34. MoU Signed for Women Internship Program (WIP), and total 39 MoUs signed with Government and Private Engineering Colleges of Ajmer, Banswara, Baran, Bhilwara, Bikaner, Bharatpur, Dholpur, Jahalawar, Jaipur, Jodhpur, Khetri, Karauli, Kota, Nathdwara, Sikar and Udaipur for implementation of Women Internship Program.

I. CAPACITY BUILDING ACTIVITIES OF PROJECT IMPLEMENTING AGENCIES

In order to develop the capacity building of the PIUs engineers, contractors' officials and other related stakeholders on compliance with social safeguards, the Safeguard Specialist-Resettlement of PMCBC frequently arranges consultations and training activities. In this context, no training organized during this reporting period for Tranche 01.

J. GRIEVANCE REDRESS MECHANISM

35. To ensure that the grievances of the affected persons are heard and resolved in a timely manner, the grievance redress mechanism (GRM) has been established for the project, which has the following approach and procedure (Figure 2)

- (i) In case the affected persons have any complaint or grievance, he/she is free to lodge his/her complaint to the site engineers of Contractor/CMSC/PIU, safeguard staff who will make efforts to resolve the complaint on the ground level itself. The project implementation unit will make efforts to redress the grievance within seven days from the receipt of the grievance.
- (ii) In case the affected persons grievance is not redressed at PIU level, the matter will be put up at the Zonal PIU level who will ensure that grievance is redressed with the time frame of seven days.
- (iii) In case the affected person's grievance is not redressed at Zonal PIU level, the matter will be put up at the PMU level who will ensure that grievance is redressed with the time frame of fifteen days.
- (iv) Affected Persons are free to approach the court of law at any time on their own will and expenses.

36. Besides the GRM of the project, the State has an online grievance monitoring system known as Rajasthan Sampark Portal. The affected persons can also lodge their complaints online at <http://sampark.rajasthan.gov.in/index.aspx>.

37. A toll-free number as mentioned in table 8 has also displayed by the contractor in a different location for lodge the grievances.

Table 8: Toll free number in each project towns

S. no	Towns	Contractors' Firm	Status of Toll-free number	Toll-free number
CMSC-II Towns				
1	Abu Road	Larsen &Toubro Ltd.	Yes	1800-180-4202
2	Sirohi	Larsen & Toubro Ltd.	Yes	1800-180-0116
3	Sardarshahar	Larsen & Toubro Ltd.	Yes	1800-833-0036
4	Ratangarh	Larsen & Toubro Ltd.	Yes	1800-313-3800
5	Laxmangarh	Larsen & Toubro Ltd.	Yes	1800-180-6322
6	Fatehpur	Larsen & Toubro Ltd.	Yes	1800-547-3900
7	Pratapgarh	Khiladi Infra Projects Ltd	Yes	1800-121-1230
8	Banswara	BIPL-SC-HP Joint Venture	Yes	1800-180-6419
CMSC-I Towns				
9	Khetri	M/s Lahoty Pvt Ltd.	Yes	1800-180-2615
10	Mandawa	M/s L N Agarwal	Yes	1800-180-2619
11	Kuchaman	M/s Larsen &Toubro Ltd.	Yes	1800-121-9400
12	Ladnu	M/s Larsen &Toubro Ltd.	Yes	1800-212-2300
13	Didwana	M/s Larsen &Toubro Ltd.	Yes	1800-212-2300
14	Makrana	M/s Larsen &Toubro Ltd.	Yes	1800-212-2300

Source: Data shared by CMSC-I & II, and compiled by PMCBC

38. A toll-free number as well as alternate number as mentioned in above table has been displayed by the contractor in different work site and office locations for lodge the grievances and complaints for any disruption during the project execution. Additionally, a toll-free number (0141-2720245) has also been displayed on RUIDP official website for lodge the grievances and complaints accordingly.

39. **Record-keeping:** PIUs, Contractor, and CMSC have been entrusted with the responsibility to maintain a proper register of the grievance (if any) which will be endorsed by all agencies involved in implementation. GRC registers are in place at the towns.


40. **Costs:** Contractors are required to be allocated budget for pamphlets and billboards as part of the EMP. Costs involved in resolving the complaints (meetings, consultations, communication and reporting/information dissemination) will be borne by the concerned PIU at

town level while costs related to escalated grievances will be met by the PMU. Cost estimates for grievance redress are included in resettlement cost estimates.

41. Office order of PMU also issued to all PIUs/CMSC to follow the grievance redress mechanism (Copy of order is attached in **Appendix 8**).

42. During the reporting period, minor complaints from the people (housekeeping, pipeline damaged, leakages in a new connection, etc.) were received, which have been resolved satisfactorily.

Figure 02: Grievance Redress Mechanism-RSTDSP

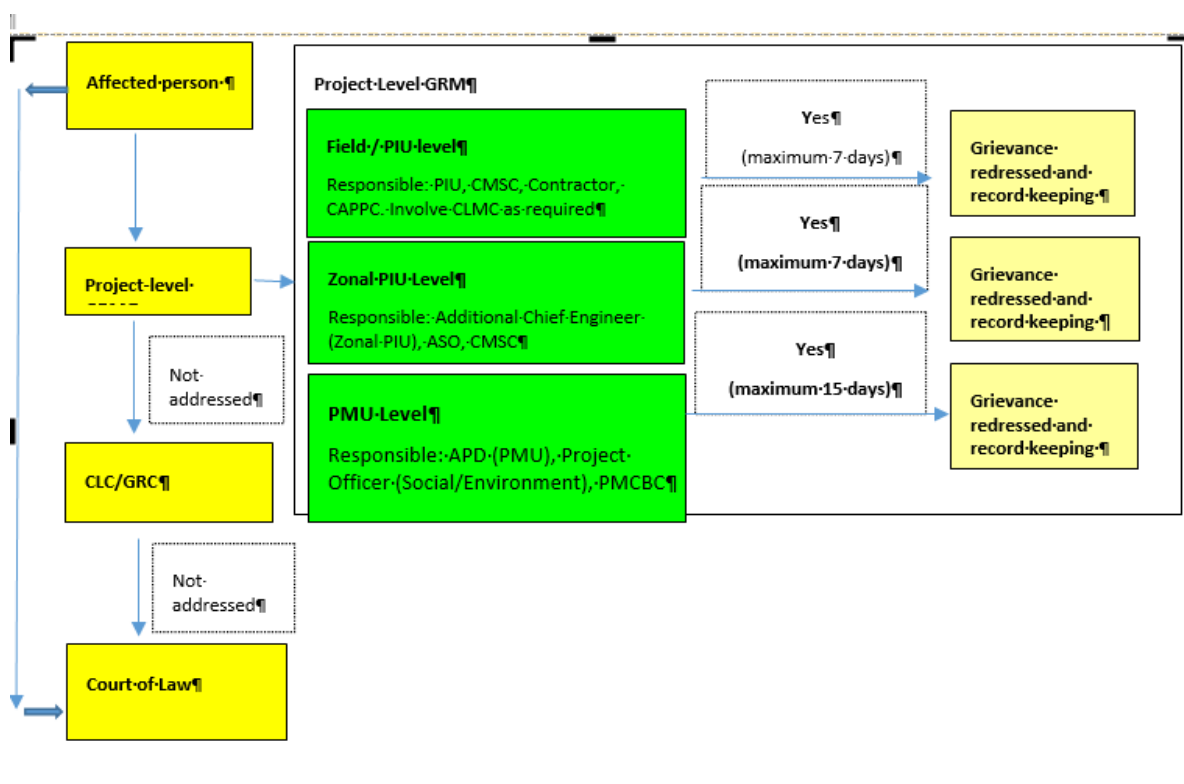

K. INSTITUTIONAL ARRANGEMENT

43. The Local Self Government Department (LSGD), Government of Rajasthan (GOR) is the executing agency (EA) of the Project, responsible for overall strategic approvals, guidance, and monitoring of the project. Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited (RUDSICO) is the Implementing Agency (IA) for the project. The Project Management Unit (PMU) is housed in the Externally Aided Projects division of RUDSICO (RUDSICO – EAP). PMU is headed by Project Director and assisted by experienced officers from engineer and finance services are responsible for the implementation of the project. Social Project Officer (SPO) at PMU assisted by Safeguard Specialist-Resettlement of Project Management Capacity Building Consultant (PMCBC) to ensure that all subprojects meet safeguard requirements as agreed in the loan covenant and in line with this RF. Two Zone office at Jodhpur and Jaipur headed by an Additional Chief Engineer (ACE) has been well

established for monitoring of PIUs. Each zonal office has one dedicated safeguard officer responsible for compliance monitoring and reporting on social, gender and environmental safeguard issues. Project implementation Unit (PIU) is well established in each subproject towns headed by Superintending Engineer/Executive Engineer for implementation of the project. One Engineer in each PIU has been designated as safety and safeguard officer who will be responsible for safeguard and health and safety requirements, monitoring and compliance. PIU is supported by CMSC in all areas of project implementation; implementation of Resettlement plan and safeguard monitoring and compliance. Deployment Status of Social Safeguards officials during the Reporting Period is presented in **Table 9** and details of Nodal officers at PIUs level is presented in **Table 10**.

Table 9: Deployment Status of Social Safeguards officials during the Reporting Period

S. no.	Name of Institution	Name of Officials	Designation	Position Filled In	Remarks
1	PMCBC	Sajal Srivastava	Safeguard Specialist-Resettlement	Yes-Intermittent	Jaipur Office
2	PMCBC	Nawal Kishor Sharma	Social Support Staff	Yes-Regular	Jaipur Office
3	CMSC-1	Nasir Hussain	Social safeguard cum Gender Professional	Yes-Regular	Jaipur Office
4	CMSC-1	Anil Kumar Pandey	Social safeguard cum Gender Professional	Yes-Regular	Jaipur Office
5	CMSC-1	Sanjiv Kumar Gupta	Social Support Staff	Yes-Regular	Jaipur Office
6	CMSC-1	Nawal Singh Kushawah	Social Support Staff	Yes-Regular	Ladnu
7	CMSC-1	Bhajan Lal Meena	Social Support Staff	Yes-Regular	Kuchaman
8	CMSC-1	Mohammad Nazir	Social Support Staff	Yes-Regular	Makrana
9	CMSC-1	Yogesh Atray	Social Support Staff	Yes-Regular	Mandawa-Khetri
11	CMSC-2	Rajeev Sharma	Social safeguard cum Gender Professional	Yes-Regular	Jodhpur Office

Source: Data shared by CMSC-I & II, and compiled by PMCBC

44. At each PIU, one engineer has been designated as a nodal officer is responsible for day to day monitoring of the environmental management plan (EMP) and implementation of resettlement plan. Nodal officers of PIU are assisting PMU SPO in the implementation of the social safeguards at the PIU level. The PIUs are responsible for the implementation of the RPs/RIPPS. PIUs will undertake internal monitoring and supervision and record observations throughout the project period to ensure that the safeguards and mitigation measures are provided as intended.

Table 10: Mobilization of Nodal officers at PIUs level

S.no	Name of Officials	PIUs at towns	Designation	Remark	Contact No
1	-	PIU, Laxmangarh	-	Sub-project is under O&M Phase.	
2	Mr. Sanju Punia	PIU, Ratangarh	SSO, PIU, Ratangarh		7726032018
3	Mr. Dinesh Phogat	PIU, Sardarshahar	SSO, PIU, Sardarshahar		8949425829
4	-	PIU, Fatehpur	-	Sub-project is under O&M Phase.	
5	Mr. Ashok Kadwasara	PIU, Sirohi	SSO, PIU, Sirohi		9929355255
6	Mr. Sunil Bishnoi	PIU, Abu Road	SSO, PIU, Abu Road		9783767531
7	Mr. Ashok Kumar	PIU, Banswara	SSO, PIU, Banswara		7976371932
8	-	PIU, Pratapgarh	-	Sub-project is under O&M Phase.	
9	Mr. Nemi Chand Panwar	PIU, Kuchaman	SSO, PIU, Kuchaman	Sub-project is under O&M Phase.	8619613736
10	Mohammad Riyaz Ahmad	PIU, Ladnun	SSO, PIU, Ladnun	Sub-project is under O&M Phase.	89554 10563
11	Mr. Rameshwar Lal	PIU, Didwana	SSO, PIU, Didwana	Sub-project is under O&M Phase.	99834 95310
12	Mr. Shrikant Yadav	PIU, Makrana	SSO, PIU, Makrana	Sub-project is under O&M Phase.	8005828897
13	Mr. Devendra Kumar Saini	PIU, Mandawa	SSO, PIU, Mandawa	Sub-project is under O&M Phase.	77373 80946
14	Mr. Devendra Kumar Saini	PIU, Khetri		Sub-project is under O&M Phase.	77373 80946

Source: Data shared by CMSC-I & II, and compiled by PMCBC

45. For monitoring of the implementation of resettlement plans, Social Safeguard staff for Project Towns are appointed by CMSC, working under the supervision and guidance of CMSC and PMCBC Social Safeguard Professionals. The task of Social Safeguard Staff assigned are as follows:

- To communicate closely with identified (identified through census survey conducted for RPs/RIPPs) potential affected persons and provide them timely information of construction schedule, distribute identification cards, educate them on their entitlements

under the RPs/RIPPs and RF, shifting affected persons during civil work execution inappropriate manner, without hampering their income or assets;

- Assist affected persons (APs) in (i) In opening bank accounts (if not already available with APs), disbursement of compensation livelihood losses and resettlement assistance (as per provisions of RF) and ensure that affected persons obtain their full entitlements under the RPs (ii) Organize consultation and discussion meetings with the affected persons the community leaders and other stakeholders throughout RP preparation and implementation phases (iii) To organize consultation and discussion meetings with the APs, the community and other stakeholders throughout RP implementation phases with proper documentation (iv) Ensure disbursement of compensation against livelihood losses, resettlement assistance (vulnerable assistance, shifting assistance, structure losses assistance, crops/trees losses assistance) as per entitlement matrix (v) Disclosure of RP, Cut of date in vernacular language at public places & project affected persons and preparation of internal RP implementation monitoring reports (vi) Distribution of one-month advance notice, to in affected areas that on the following date the civil works will be started in following areas and timely shifting of squatters and encroachers from temporary impact zone during construction if required (vii) Registering grievances of affected persons (the grievance redress mechanism (GRM) already established) and assist to PIU in resolving grievances at PIU level or GRM level (viii) Assist the affected persons in the redress of grievances through the Grievance Redress mechanism established as part of the RP/RIPP, and make the affected persons aware of GRM at several levels (ix) Assist affected persons in getting benefits from various government development programs particularly for income restoration/ generation.

46. Social Outreach Team (SOT) has been mobilized in project towns for supporting the Social Safeguard Staff of CMSC in the implementation of resettlement plan and community awareness activities. Status of SoT in subproject wise is given **Table 11**.

Table 11: Present Status of SOT

S.no	Town/	Staff Deployed in SOT	Contractors' Firm
1	Abu Road	02	M/s Larsen &Toubro Ltd.
2	Sirohi	02	M/s Larsen & Toubro Ltd.
3	Sardarsahar	04	M/s Larsen & Toubro Ltd.
4	Ratangarh	04	M/s Larsen & Toubro Ltd.
5	Laxmangarh	0	M/s Larsen & Toubro Ltd.
6	Fatehpur	0	M/s Larsen & Toubro Ltd.
7	Pratapgarh	0	M/s Khiladi Infra Projects Ltd
8	Banswara	04	M/s BIPL-SC-HP Joint Venture
9	Kuchaman	03	M/s Larsen &Toubro Ltd.

S.no	Town/	Staff Deployed in SOT	Contractors' Firm
10	Makrana	02	M/s Larsen &Toubro Ltd.
11	Ladnu	01	M/s Larsen &Toubro Ltd.
12	Didwana	0	M/s Larsen &Toubro Ltd.
13	Khetri	02	M/s Lahoty Pvt Ltd.
14	Mandawa	05	M/s L N Agarwal

Source: Data shared by CMSC-I & II, and compiled by PMCBC

L. MONITORING RESULTS-FINDINGS

47. The project monitoring using specific indicators e.g. number of days for which compensation paid versus number of actual days of disruption; number of vulnerable households provided vulnerable assistance; number of grievances registered versus resolved and unresolved grievances; compensations cost versus payments made and so on to get overall understanding about the current status. In addition, compensation and payments of all types of impacts and losses; progress of additional compensation to vulnerable persons; types of training and number of participants; employment opportunities available and availed by vulnerable groups; status of consultations and redress of grievances; status of inclusion and participation, particularly affected vulnerable groups; social safeguard concerns in construction sites; status and dates of disclosure of RPs/RIPPs.

48. Social safeguards activities have been carried in the period that illustrated the following Table 12.

Table-12: Status of Monitoring of the Sub-projects (October 2024 –March 2025)

S. N.	Resettlement Plan Activities	Status	Remarks
A. Pre-Construction Activities and Resettlement Plan Activities			
1	Approval of final RPs/RIPPs by ADB prior to contract award	All the draft RPs/RIPPs/DDR's have been updated based on 100% survey of potential affected persons and same has been submitted to ADB.	Contracts for all the 14 towns have been awarded and pipe laying work for waste water and water supply networks has been progressed considerably in all the towns. Approval has been obtained for Abu Road, Sirohi, Laxmangarh, Ratangarh, Sardarsahar, Pratapgarh, Mandawa, Khetri and Makrana.
2	Disclosure of final Resettlement Plan on ADB and EA websites	Updated RPs/RIPPs of Abu Road, Sirohi, Laxmangarh, Ratangarh, Sardarsahar, Pratapgarh, Mandawa, Khetri and Makrana has been disclosed in ADB and EA website.	RIPP of Banswara and RPs of Ladnu & Kuchaman, and DDRs of Didwana and Fatehpur are under review by ADB. After approval, the same will be disclosed on ADB and EA website.
3	Circulation of summary Resettlement Plan in local languages to all stakeholders	Summary of RF and entitlement provision for losses was circulated to potential affected persons and other stakeholders before starting of survey.	
Resettlement Plan Implementation			
1	Grievance	Grievance Redress Mechanism has	Office order of PMU issued on dated

S. N.	Resettlement Plan Activities	Status	Remarks
	Redress Mechanism established at different levels	been well established at different levels.	18.12.2020. A toll-free number/ complaint number has also been displayed by the contractors in all the project towns at different location for lodge the grievances/ complaints.
2	Entitlements and grievance redress procedure disclosed	Entitlement provision for losses process for lodging grievances has been circulated in project towns.	
3	Finalization of list of affected persons, vulnerable affected persons and compensation due	List of potential affected persons along with vulnerability status has been finalized in all the 11 th towns where IR impact was envisaged.	A total 3221 affected persons incorporating 1286 vulnerables has been identified in 11 project towns, and compensation to APs have been completed in 10 towns. Compensation disbursement is pending for 15 APs in Kuchaman only due to work has not been started in APs area.
4	Finalization of list of roads for full or partial closure; mitigation measures proposed and implemented (with photographic documentation)	Presently no such issues are encountered in any town.	If road closure will be required in any subprojects, mitigation measures along with photographs shall be provided to ADB.
5	Number of days roads were closed (full and partial closure)	Presently no such issues are encountered in any town.	
6	Affected persons received entitlements as per EM in RP	Up to March 2025, a total no. of 2033 affected persons including 819 vulnerable APs has been compensated and amount of Rs 1,94,21,284 has been disbursed. Vulnerable affected persons have communicated for jobs in construction activities, but they have not showing interest.	
7	Additional assistance (project-related construction jobs, if willing and able) for vulnerable households given (No. of vulnerable affected persons assisted)		
8	Grievances No. of grievances registered No. of grievances redressed Outstanding complaints Disclosure of grievance redress statistics	During the reporting period, minor complaints from the people (housekeeping, pipeline damaged, leakages in a new connection, etc.) were received, which have been resolved satisfactorily.	
9	Consultation, participation and	Yes consultation, participation, and disclosure have been taken place as	

S. N.	Resettlement Plan Activities	Status	Remarks
	disclosure as per Plan	per Plan	
C. Monitoring			
11	Survey on satisfaction levels of affected persons with Resettlement Plan implementation completed	Feedback taken from affected persons, who have been compensated from the project. All have been utilized the respective amount in their businesses.	

M. COMPLIANCE STATUS OF LOAN COVENANTS

49. The covenants to the loan agreement with ADB require that implementation of the project that “projects are designed, constructed, operated and maintained in accordance with ADB’s Safeguard Policy Statements (2009) and agreed between the Borrower and ADB.” Covenants written into the loan agreement that are related to social safeguards are laid in Table 13. These refer to actions that have been compiled satisfactory during the reporting period.

Table 13: Status of Loan Covenants

Covenant	Status of Compliance
<u>Implementation Arrangements</u> 1. The Borrower, the State and the EA shall ensure that the Project is implemented in accordance with the detailed arrangements set forth in the PAM. Any subsequent change to the PAM shall become effective only after approval of such change by the Borrower, the State, EA and ADB. In the event of any discrepancy between the PAM and this Loan Agreement, the provisions of this Loan Agreement shall prevail.	Being Complied
2. (a) The Borrower shall ensure or cause the EA to ensure, towards smooth implementation of the Project, that grievances if any from stakeholders, relating to Project implementation or use of funds under the Project are addressed effectively and efficiently.	Being Complied. For the development of pamphlets and billboards (containing contact number of person) where grievances can be lodge) that will be displayed at site are considered under EMP. Costs involved in resolving the complaints (meetings, consultations, communication and reporting/information dissemination) will be borne by the concerned PIU at town level while costs related to escalated grievances will be met by the PMU. Office order of GRC issued on 18.12.2020 and well established in the towns. The GRM is progressively functioning in all the Town.
2 (b) The Borrower shall ensure or cause the State and EA to ensure compliance with all the requirements and	Will be complied

Covenant	Status of Compliance
obligations in their part as included in this Loan Agreement and the Project Agreement to meet the objectives of the Project in a timely and efficient manner.	
3. The Borrower shall ensure or cause the EA to ensure that its PMU, Zonal Project Offices, and its PIUs within the Project ULBs, employ sufficient staff including increasing the number of adequate staff as included in the PAM, with relevant expertise in the fields of project management, financial management, engineering, procurement, operations and management, and environmental and social safeguards implementation. The EA will ensure that the PMU, Zonal Offices, and the PIUs housed in the Project ULBs, are equipped with the necessary staff, office space, facilities, equipment, support staff and management information systems for the entire duration of the Project and thereafter.	Complied/Being Complied.
4. The Borrower shall ensure or cause the EA to ensure that towards smooth implementation of the Project, grievances if any from stakeholders relating to the Project implementation or use of funds are addressed effectively and efficiently.	Costs involved in resolving the complaints (meetings, consultations, communication and reporting/information dissemination) will be borne by the concerned PIU at town level while costs related to escalated grievances will be met by the PMU. Office order of GRC issued on 18.12.2020 and well established in project towns. The GRM is progressively functioning in all the Town.
<p><u>Land Acquisition and Involuntary Resettlement</u></p> <p>The Borrower shall ensure or cause the EA to ensure that all land and all rights-of-way required for each Subproject are made available to the Works contractor in accordance with the schedule agreed under the related Works contract and all land acquisition and resettlement activities are implemented in compliance with (a) all applicable laws and regulations of the Borrower and the State relating to land acquisition and involuntary resettlement; (b) the Involuntary Resettlement Safeguards; (c) the RF; and (d) all measures</p>	<p>Land acquisition is not required as all construction works are proposed in government land identified and already provided by line department.</p> <p>Involuntary resettlement impacts are confined to mainly temporary loss of livelihood due to temporarily displacement from the location of business of mobile vendor or due to loss of access to shops, all losses are temporary in nature.</p>
<p>Without limiting the application of the Involuntary Resettlement Safeguards, the RF or the RP/RIPP as applicable, the Borrower shall ensure or cause the EA to ensure that no physical or economic displacement takes place in connection with any Subproject until:</p> <p>(a) compensation and other entitlements have been provided to affected people on the related Works contract/section thereof in accordance with the relevant RP/RIPP as applicable; and</p> <p>(b) a comprehensive income and livelihood restoration program has been established in accordance with the relevant RP/RIPP as applicable.</p>	Noted. Will be complied.
<p><u>Indigenous Peoples</u></p> <p>The Borrower shall ensure or cause the EA to ensure that the preparation, design, construction, implementation and operation of the Subprojects and Project facilities comply with (a) all applicable laws and regulations of the Borrower and the State relating to indigenous peoples; (b) the Indigenous Peoples Safeguards; (c) the IPPF; and (d) all measures and requirements set forth in the relevant RIPP if any as required, and any corrective or preventative actions</p>	Noted. Will be complied.

Covenant	Status of Compliance
set forth in a Safeguards Monitoring Report. No Category A subprojects will be financed under the Project..	
Notwithstanding the stipulation that no Category A Subprojects under environment, involuntary resettlement or indigenous people, will be financed under the Project, in the unforeseen situation of change in categorization of a Subproject that is under implementation, to Category A, the Borrower shall ensure or cause the EA to ensure, in consultation with ADB that such Subproject shall be completed in full compliance of the ADB Safeguard Policy requirements and applicable laws and regulations of the Borrower and the State.	
<u>Human and Financial Resources to Implement Safeguards Requirements</u> The Borrower shall ensure or cause the EA to ensure that all necessary budgetary and human resources to fully implement the EMPs, the RPs and any RIPPs (as applicable) are made available on a timely basis.	Noted. being complied. R&R budget head has been allotted and shared with PIUs for timely disbursement of compensation to potential APs.
<u>Safeguards – Related Provisions in Bidding Documents and Works Contracts</u> (a) The Borrower shall ensure or cause the EA to ensure that all bidding documents and contracts for Works contain provisions that require contractors to: (b) comply with the measures and requirements relevant to the contractor set forth in the IEE, the EMP, the RP(s) and any RIPP, if any (to the extent they concern impacts on affected people during construction), and any corrective or preventative actions set out in a Safeguards Monitoring Report; © make available a budget for all such environmental and social measures; (d) provide the EA with a written notice of any unanticipated environmental, resettlement or indigenous peoples risks or impacts that arise during construction, implementation or operation of the Project that were not considered in the IEE, the EMP, the RP/RIPP (as applicable); (e) adequately record the condition of roads, agricultural land and other infrastructure prior to starting to transport materials and construction; and (f) fully reinstate pathways, other local infrastructure, and agricultural land to at least their pre-project condition upon the completion of construction.	Noted. being complied
<u>Safeguards Monitoring and Reporting</u> (a) The Borrower shall ensure or cause the EA to ensure the following: (a) submit semiannual Safeguards Monitoring Reports to ADB and disclose relevant information from such reports to affected persons promptly upon submission; (b) if any unanticipated environmental and/or social risks and impacts arise during construction, implementation or operation of the Project that were not considered in the IEEs, the EMPs, the RPs or any RIPP (as applicable), promptly inform ADB of the occurrence of such risks or impacts, with detailed description of the event and proposed corrective action plan; and (c) report any breach of compliance with the measures and requirements set forth in the relevant EMP, the RP or RIPP (as applicable) promptly after becoming aware of the breach.	Noted. being complied

N. FOLLOW UP ACTIONS, RECOMMENDATION AND DISCLOSURE

50. By the end of this reporting period (October 2024-March 2025), Contracts for all the 14 towns have been awarded and pipe laying work for waste water and water supply networks has been progressed considerably in all the towns. Resettlement assistance of ₹ 1,94,21,284 has been paid to 2033 number of affected persons. During the reporting period, minor complaints from the people (housekeeping, pipeline damaged, leakages in a new connection, etc.) were received, which have been resolved satisfactorily.

51. The following Table 14 shows the issues and recommendations that are expected to be accomplished by the PIUs under RSTDSP. CMSC and contractors with the support of PMCBC and PMU to perform the activities from October 2024 to March 2025.

Table-14: Issues and Recommendations

Activity/Key Issues	Recommended Action	Responsibility	Action Taken Till March 2025
Updating RPs/RIPPs/DDR as per final scope of works frizzed in SIP.	Due diligence (a joint site visit) will be undertaken by CMSC/PIU along with a safeguard consultant (PMCBC) for additional or changed works, if are proposed in SIP.	CMSC-1&2/ PMCBC/Contractors /PIU	RPs/RIPPs/DDR are being updated to reflect these changes in the project scope and updated documents are being submitted to ADB.
Implementation of RPs/RIPPs	Affected persons will be compensated prior to the commencement of civil works in the particular stretches where they are running their livelihood activities.	CMSC-1&2/ Contractors/ /PIUs	RPs /RIPPs are implemented before starting civil work.
Collect data and visit to monitor of the social safeguard activities at field level	Social Safeguard Professional of CMSC/ PMCBC	PIUs/PMU	PMU/PIU, PMCBC and CMSC team is visiting work sites at frequently for compliance of safeguard issues.
Conduct and participate coordination meeting/ training on social safeguards at PIUs level	Coordination meeting/ training on social safeguards at PIUs level	CMSC-1&2/ Contractors /PIUs/PMCBC	Meetings and trainings related to social safeguard requirement with implementing agency are being done at regular basis.

Appendix 1: Progress and Status of subprojects –RSTDSP

S No.	Town		Package No.	Name of Contractor	NTP Date	Contract Cost (INR)	Contract Cost (US\$)*	Physical Progress (Upto March 2025)
1	Sardarshahar	W/S & W/W	RSTDIP/ SRD/01	M/s Larsen & Toubro Limited	15.6.2020	196,70,00,000.00	258,87,437.68	77%
2	Abu Road	W/S & W/W	RSTDIP/SHR-ABR/01	M/s Larsen & Toubro Limited	18.6.2020	263,77,98,830.00	345,87,823.18	88%
3	Sirohi	W/S & W/W		M/s Larsen & Toubro Limited	18.6.2020	213,92,01,170.00	280,50,020.71	91%
4	Banswara	W/S & W/W	RSTDIP/BNS/04	M/s. BIPL-SC-HP Joint Venture	11.02.2021	320,74,60,597.00	435,81,759.39	99%
5	Khetri	W/S & W/W	RSTDIP/KTR/03	M/s. Lahoty-LNA (JV)	20.03.2021	79,63,81,137.50	109,93,392.45	73%
6	Mandawa	W/S & W/W	RSTDIP/MDW/03	M/s Larsen & Toubro Limited	08.03.2021	106,12,15,221.40	14,502,032.35	89%
7	Kuchaman	W/S & W/W	RSTDIP/KMN/02	M/s Larsen & Toubro Limited,	05.05.2021	313,93,75,000.00	42,458,412.22	82%
8	Ratangarh	W/W	RSTDIP/ RTG-FTP-LXG/01	M/s Larsen & Toubro Limited	15.6.2020	182,44,31,237.00	240,11,108.26	85%
9	Laxmangarh	W/S		M/s Larsen & Toubro Limited	15.6.2020	49,45,94,511.00	650,92,95.66	100%
10	Fatehpur	W/W		M/s Larsen & Toubro Limited	15.6.2020	114,89,74,252.00	151,21,504.49	100%
11	Pratapgarh	W/W	RSTDIP/PRT/01	M/s. Khilari Infrastructure Pvt. Ltd.	28.10.2020	190,60,00,255.00	257,45,696.51	100%
12	Didwana	W/W	RSTDIP/LDN-DID-MKN/01	M/s Larsen & Toubro Limited	05.05.2021	87,39,66, 167.00	11,819,457.78	91%
13	Makrana	W/W		M/s Larsen & Toubro Limited	05.05.2021	142,98,18,867.00	19,336,771.12	92%
14	Ladnun	W/W		M/s Larsen & Toubro Limited	05.05.2021	174,40,93,122.00	23,586,994.33	75%

Source: Monthly Progress Report (MPR) March- 2025

Appendix 2- Details of Payment disbursed during this reporting period

Kuchman- Payment Disbursed to 5 APs

Office Order of 5 Aps



कार्यालय अधीक्षण अभियंता
आरयूआईडीपी, कुचामन, नागौर (राज.)

Email id- kmn.ruidp@rajasthan.gov.in

कार्यालय पता-प्लॉट सं.21, देवनगर, एस.के.डिफेंस ऐकडमी के पास, झालरा रोड, कुचामन 341508

क्रमांक.-आरयूआईडीपी/लेखा/2024-25/ 1783

दिनांक:- 10-8-2024

कार्यालय आदेश

श्रीमान अतिरिक्त परियोजना निदेशक आरयूआईडीपी, जयपुर के पत्रांक F3(301)(60) RUIDP/PIU/KMN/PH-IV / ADB S.S./ Gen/Adm/2020-21/3914-27 दिनांक 14.07.2021 एवं F3(301)(60) RUIDP/PIU/KMN/PH-IV / ADB S. S./ Gen/Adm/2020-21/4969 दिनांक 12.08.2021 की अनुपालना में कुचामन शहर में जलप्रदाय एवं सिंचन कार्य के अंतर्गत सज्जीमण्डी के अन्दर दोनों तरफ एवं सीकर रोड से सीकर बस स्टैण्ड रोड सहक के दोनों ओर (गोल प्याउ एवं शिव मेडिकल के पास) के कतार में जो Vendors या फुटपाथ पर व्यवसाय कर रहे हैं उनको कार्य के दौरान अन्यत्र स्थानान्तरण की आवश्यकता के मध्य नजर उनके व्यवसाय पर होने वाले प्रभाव एवं कार्य बिना किसी व्यवधान के सम्पादित हो जिसके लिए संयुक्त मौका निरीक्षण रिपोर्ट के आधार पर माईकोप्लान के अनुसार निम्नानुसार व्यक्तियों को उनके नाम के आगे उल्लेखित राशि को भुगतान करने की स्वीकृति प्रदान की जाती है।

S.R. No.	R.P. No.	Aps Placed Verified	Name As in Bank of Affected Person	Amt. (RS.)	Mobile No.	Name of Bank	Account No.	Branch	IFSC Code
1	92	Right	Madan Lal	16100	9571033588	UCO BANK	13570110056936	Mathania	UCBA0001357
2	173	Right	Dhapali Devi	14700	8769024433	Bank of Baroda	54980100003877	Kuchaman	BARBOKUCHAM
3	181	Right	Gajanand	6400	8290400686	State Bank of India	61202635529	Kuchaman	SBIN0031733
4	188	Right	Kamla Devi	14700	8302337754	Bank of Baroda	54988100000104	Kuchaman	BARBOKUCHAM
5	198	Right	Javed	7100	9057246991	UCO BANK	03823211106234	Kuchaman	UCBA0000382
6	199	Right	Saddam Husain	5700	7737714132	UCO Bank	03823211116318	Kuchaman	UCBA0000382
7	208	Right	Mohammad Hussain	7100	9829178532	UCO BANK	03820110016466	Kuchaman	UCBA0000382
8	215	Right	Manbhari Devi	14700	9785987576	Punjab National Bank	17452121011104	Kuchaman	PUNB0174510
9	216	Right	Mohan Ram	7100	8875066905	Central Bank of India	3041878678	Kuchaman	CBIN0280439
10	238	Left	Mohammad Javed	6400	8385017786	Central Bank of India	3843043024	Kuchaman	CBIN0280439
11	274	Right	Shahrukh Khan	7100	8740086311	State Bank of India	61154793442	Kuchaman	SBIN0031733
12	279	Right	Ganga Devi	14700	8890288057	Central Bank of India	1533894459	Kuchaman	CBIN0280439
13	281	Right	Kistur Mal	5700	9828607807	Punjab National Bank	17452191021263	Kuchaman	PUNB0174510
14	299	Right	Dharina Ram	7800	9024604477	State Bank of India	41251145285	Kuchaman	SBIN0031733
15	301	Right	Pappu Lal	5700	7665660090	UCO BANK	03823211077459	Kuchaman	UCBA0000382
16	302	Right	Bhanwar Lal	5700	9261791590	State Bank of India	61212965169	Kuchaman	SBIN0031733
17	306	Right	Chhagan Lal	5700	8696585261	State Bank of India	51046290720	Kuchaman	SBIN0031733
18	309	Right	Gopal Lal	5700	8058306271	Punjab National Bank	7558000100030773	Kuchaman	PUNB0755800
19	312	Right	Savita	14700	9828708551	Central Bank of India	5340740633	Jillya	CBIN0282492
20	315	Right	Kani	14700	9982259483	Punjab National Bank	17452121003932	Kuchaman	PUNB0174510



कार्यालय अधीक्षण अभियंता आरयूआईडीपी, कुचामन, नागौर (राज.)

Email Id- kmn.ruidp@rajasthan.gov.in

कार्यालय पता-प्लॉट सं.21, देवनगर, एस.के.डिफेंस एकेडमी के पास, झालारोड, कुचामन 341508

21	321.	Left	Mo. Aslam Pathan	5700	8107436578	IDFC Frist Bank	10179967377	Kuchaman	IDFB0043312
22	325	Right	Ranjit Kasotiya	5700	7014729696	State Bank of India	61207895797	Kuchaman	SBIN0031733
23	328	Right	Gopal Lal	7100	9549493188	State Bank of India	61260437680	Kuchaman	SBIN0031733
24	329	Right	Lalit Kumar	5700	8502993126	Bank of India	747510110001392	Kuchaman	BKID0007475
25	330	Left	Ramjan Shekh	5700	7357542077	State Bank of India	42237087888	Kuchaman	SBIN0031733
26	341	Left	Shri Bhagwan Agarwal	5700	9529683568	State Bank of India	51046289828	Kuchaman	SBIN0031733
27	342	Left	Gopal	5700	9982124960	Central Bank of India	1533891072	Kuchaman	CBIN0280439
28	343	Right	Manjur	5700	9829717074	State Bank of India	34613202160	Kuchaman	SBIN0011400
29	361	Right	Sohani Devi	14700	6367582477	Central Bank of India	3453557883	Kuchaman	CBIN0280439
Grand Total Rs.				249200	Rupees Seven Lakh Forty Nine Thousand Two Hundred Only/-				

(अशोक कुमार जैन)
अधीक्षण अभियंता

आरयूआईडीपी, (पीआईयू) कुचामन

दिनांक :- 10.9.2024

क्रमांक :- 1724-1731

प्रतिलिपी उचित कार्यवाही एवं सूचनार्थ प्रेषित है :-

1. श्रीमान् अति:परियोजना निदेशक आरयूआईडीपी, जयपुर।
2. श्रीमान् अति:मुख्य अभियन्ता आरयूआईडीपी, जयपुर।
3. श्रीमान् उप कोषाधिकारी कुचामन।
4. श्रीमान् सहायक लेखाधिकारी कुचामन।
5. श्रीमान् अधिषाशी अभियन्ता आरयूआईडीपी, कुचामन।
6. श्रीमान् टीमलीडर सीएमसी-01 जयपुर।
7. श्रीमान् सहायक निर्माण अभियन्ता सीएमएससी-01।
7. कार्यालय रक्षित पत्रावली।

(अशोक कुमार जैन)
अधीक्षण अभियंता

आरयूआईडीपी, (पीआईयू) कुचामन



कार्यालय अधीक्षण अभियंता आरयूआईडीपी, कुचामन, नागौर (राज.)

Email Id- kmn.ruidp@rajasthan.gov.in

कार्यालय पता-प्लॉट सं.21, देवनगर, एस.के.डिफेंस एकेडमी के पास, झालारोड, कुचामन 341508

क्रमांक:-आरयूआईडीपी/लेखा/2024-25/1754

दिनांक:- 11.9.2024

कार्यालय आदेश

श्रीमान् अतिरिक्त परियोजना निदेशक आरयूआईडीपी, जयपुर के फॉक F3(301)(60) RUIDP/PIU/KMN/PH-IV / ADB S.S./ Gen/Adm/2020-21/3914-27 दिनांक 14.07.2021 एवं F3(301)(60) RUIDP/PIU/KMN/PH-IV / ADB S.S./ Gen/Adm/2020-21/4969 दिनांक 12.08.2021 की अनुमतिना मे कुचामन शहर मे जलप्रदाय एवं सिंचन कार्य के अर्न्तगत सञ्जीवनी के अन्दर दोनो तरफ एवं सीकर रोड से सीकर बस स्टैण्ड रोड सड़क के दोनो ओर (गोल प्याउ एवं शिव मैडिकल के पास) दोनो तरफ एवं चुंगी रोड के कतार मे जो Vendors या फुटपाथ पर व्यवसाय कर रहे है उनको कार्य के दौरान अन्यत्र स्थानान्तरण की आव यकता के मध्य नजर उनके व्यवसाय पर होने वाले प्रभाव एवं कार्य बिना किसी व्यवधान के सम्पादित हो जिसके लिए संयुक्त मंडल निरीक्षण रिपोर्ट के आधार पर माईकोपलान के अनुसार R.P. No. 39,257,282,360 (R.P. No. 39Faruk Rs.7100/-) (R.P.No.257 Ramkavari 14700/-) (R.P.No.282 Kiran Devi 14700/-) (R.P.No.360 Bodu Ram 5700/-) के बैंक दिवर्ण को पे मैनेजर द्वारा अस्थीकृत किये जाने के कारण निम्न R.P. No. 39,257,282,360 को छोडकर उपरोक्त सारणी अनुसार भुगतान किये जाने की स्वीकृति प्रदान की जाती है। R.P. No. 39,257,282,360 प्रभावित व्यक्तियों द्वारा उचित बैंको का दिवर्ण प्रस्तुत करने पर पृथक से कार्यालय आदेश जारी कर भुगतान करवा दिया जायेगा। निम्नांकित व्यक्तियों को उनके नाम के आगे उल्लेखित राशि को भुगतान करने की स्वीकृति प्रदान की जाती है।

S.R No.	R.P. No.	Aps Placed Verified	Name As in Bank of Affected Person	Amt. (RS.)	Mobile No.	Name of Bank	Account No.	Branch	IFSC Code
1	77	Left	Mo.Imran	7100	9828645688	State Bank of India	61142788357	Kuchaman	SBIN0031733
2	86	Right	Kailash C.Kumawat	5700	9610355880	Punjab National Bank	7558000100020563	Kuchaman	PUNB0755800
3	97	Right	Monu	5700	9521186568	UCO BANK	03823211116660	Kuchaman	UCBA0000382
4	104	Left	Sushila Devi	15400	8955795193	Central Bank of India	3692052302	Kuchaman	CBIN0280439
5	113	Right	Ramesh Sharma	5700	9636284416	State Bank of India	34709832830	Kuchaman	SBIN0011400
6	121	Right	Rajendra Kumar	5700	9864859663	Central Bank of India	3950414420	Molasar	CBIN0280443
7	169	Left	Sundri Devi	14700	9079060122	Central Bank of India	1533763052	Kuchaman	CBIN0280439
8	195	Right	Ramjan	5700	9251276891	Punjab National Bank	7558000100027540	Kuchaman	PUNB0755800
9	205	Left	Deepak	7100	9680428267	UCO BANK	03823211116301	Kuchaman	UCBA0000382
10	255	Right	Mumtaj Ali	7100	9829671286	Punjab National Bank	17452191022529	Kuchaman	PUNB0174510
11	269	Left	Chauthi Devi	14700	7073481338	Central Bank of India	3580015502	Kuchaman	CBIN0280439

(अशोक कुमार जैन)



कार्यालय अधीक्षण अभियंता आरयूआईडीपी, कुचामन, नागौर (राज.)

Email id- kma.ruidp@rajasthan.gov.in

कार्यालय पता-प्लॉट सं.21, देवनगर, एस.के.डिफेंस एकेडमी के पास, झालारोड, कुचामन 341508

12	273	Right	Aslam Ali	5700	7014729549	Central Bank of India	5179518320	Kuchaman	CBIN0280439
13	308	Right	Bidami Devi	5700	9571033588	UCO BANK	03823211104667	Kuchaman	UCBA0000382
14	311	Right	Pusi Devi	14700	7615042704	State Bank of India	61288561418	Kuchaman	SBIN0031733
15	313	Right	Sohani Devi	14700	8094679872	UCO BANK	03820110089125	Kuchaman	UCBA0000382
16	319	Left	Chhoti Devi	14700	9828849837	Central Bank of India	5648337806	Jilija	CBIN0282492
17	327	Right	Ganpat Lal	5700	9829965743	Bank of India	747510110002075	Kuchaman	BKID0007475
18	338	Right	Hamid	5700	9694916284	UCO BANK	03823211092032	Kuchaman	UCBA0000382
Grand Total Rs.				161500	Rupees One Lakh Sixty One Thousand Five Hundred Only/-				

(Signature)

(अशोक कुमार जैन)

अधीक्षण अभियंता
आरयूआईडीपी, (पीआईयू) कुचामन

दिनांक :- 11.9.2024

क्रमांक :- 1755-1762

प्रतिलिपी उचित कार्यवाही एवं सूचनाएं प्रेषित है :-

1. श्रीमान् अति:परियोजना निदेशक आरयूआईडीपी, जयपुर।
2. श्रीमान् अति:मुख्य अभियन्ता आरयूआईडीपी, जयपुर।
3. श्रीमान् उप कोषाधिकारी कुचामन।
4. श्रीमान् सहायक लेखाधिकारी कुचामन।
5. श्रीमान् अधिशाषी अभियन्ता आरयूआईडीपी, कुचामन।
6. श्रीमान् टीमलीडर सीएमसी-01 जयपुर।
7. श्रीमान् सहायक निर्माण अभियन्ता सीएमएससी-01।
7. कार्यालय रक्षित पत्रावली।

(Signature)

अधीक्षण अभियंता
आरयूआईडीपी, (पीआईयू) कुचामन



कार्यालय अधीक्षण अभियंता आरयूआईडीपी, कुचामन, नागौर (राज.)

Email id- kma.ruidp@rajasthan.gov.in

कार्यालय पता-प्लॉट सं.21, देवनगर, एस.के.डिफेंस एकेडमी के पास, झालारोड, कुचामन 341508

क्रमांक:-आरयूआईडीपी/लेखा/2024-25/1763

दिनांक:- 11.9.2024

कार्यालय आदेश

श्रीमान् अतिरिक्त परियोजना निदेशक आरयूआईडीपी, जयपुर के पत्रांक F3(301)(60) RUIDP/PIU/KMN/PH-IV / ADB S.S./ Gen/Adm/2020-21/3914-27 दिनांक 14.07.2021 एवं F3(301)(60) RUIDP/PIU/KMN/PH-IV / ADB S.S./ Gen/Adm/2020-21/4969 दिनांक 12.08.2021 की अनुपालना में कुचामन शहर में जलप्रदाय एवं सिंचन कार्य के अन्तर्गत सञ्जीमण्डी के अन्दर दोनों तरफ एवं पुराना बस स्टैंड, गोल प्याच, शिव मेडिकल के पास एवं सीकर रोड के दोनों तरफ के कतार में जो Vendors या फुटपाथ पर व्यवसाय कर रहे हैं उनको कार्य के दौरान अन्यत्र स्थानान्तरण की आवश्यकता के मध्य नजर उनके व्यवसाय पर होने वाले प्रभाव एवं कार्य बिना किसी व्यवधान के सम्पादित हो जिसके लिए संयुक्त मौका निरीक्षण रिपोर्ट के आधार पर माईकोप्लान के अनुसार भुगतान हेतु प्रस्तावित R.P. No. 192 (R.P. No. 192 Dilip Kumawat Rs.5700/-) के बैंक विवरण को पे मैनजर द्वारा अस्वीकृत किये जाने के कारण निम्न R.P. No. 192 को छोड़कर उपरोक्त सारणी अनुसार भुगतान किये जाने की स्वीकृति प्रदान की जाती है। R.P. No. 192 द्वारा उचित बैंक का विवरण प्रस्तुत करने पर पृथक से कार्यालय आदेश जारी कर भुगतान करवा दिया जायेगा। निम्नानुसार व्यक्तियों को उनके नाम के आगे उल्लेखित राशि को भुगतान करने की स्वीकृति प्रदान की जाती है।

S.R No.	R.P. No.	Aps Placed Verified	Name As in Bank of Affected Person	Amt. (RS.)	Mobile No.	Name of Bank	Account No.	Branch	IFSC Code
1	91	Left	Kanchan	5700	6367382575	UCO Bank	03823211076636	Kuchaman	UCBA0000382
2	122	Right	Mangna Ram	7100	9680543440	SBI	34311912037	Kuchaman	SBIN0011400
3	134	Right	Setu	5700	9649022882	Punjab National Bank	174510010001768'3	Kuchaman	PUNB0174510
4	137	Right	Sunil Damami	5700	9521542962	UCO Bank	03823211124498	Kuchaman	UCBA0000382
5	153	Right	Shivraj Sain	5700	9983263691	Central Bank of India	2953789675	Kuchaman	CBIN0282492
6	162	Right	Radheshyam	14700	9530649876	Central Bank of India	4063590100	RAUN	CBIN0281684
7	166	Right	Manoj Kumar Jain	7100	8949092389	UCO Bank	16000110069837	Kuchaman	UCBA0001600
8	193	Right	Mahesh Kumar	5700	8385017812	State Bank of India	61163958554	Kuchaman	SBIN0010733
9	232	Right	Raju Munawat	5700	9694174500	Bandahan Bank	50090003606011	Kuchaman	BDBL0001567
10	233	Right	Tikam Chand	5700	9829529282	Central Bank of India	1533780101	Kuchaman	CBIN0280439
11	298	Right	Rajesh	7100	8305967191	Central Bank of India	3755801397	Mihona	CBIN0280784
12	300	Right	Soyab Akhtar	5700	9549998585	UCO Bank	038232111042556	Kuchaman	UCBA0000382
13	303	Right	Raphik	5700	7378126324	SBI	31069030548	Kuchaman	SBIN0011400
14	304	Right	Mohammad Gufran	7100	7340436186	UCO Bank	03823211110583	Kuchaman	UCBA0000382
15	320	Left	Tofik Pathan	5700	9116928859	SBI	34922920983	Kuchaman	SBIN0011400

(Signature)



कार्यालय अधीक्षण अभियंता
आरयूआईडीपी, कुचामन, नागौर (राज.)

Email id- kmn.rudp@rajasthan.gov.in

कार्यालय पता-प्लॉट सं.21, देवनगर, एस.के.डिफेंस ऐकेडमी के पास, झालरारोड, कुचामन 341508


16	324	Right	Taruf	5700	8279214269	Central Bank of India	1533893080	Kuchaman	CBIN0280439
17	351	Right	Uma Shankar	7100	8824729227	Indian Bank	59120626603	Sirsa Kalar	IDIB000J541
				112900	Rupees One Lakh Twelve Thousand Nine Hundred Only/-				

क्रमांक :-


1764-1770

प्रतिलिपी उचित कार्यवाही एवं सूचनार्थ प्रेषित है :-

1. श्रीमान् अति.परियोजना निदेशक आरयूआईडीपी, जयपुर।
2. श्रीमान् अति.मुख्य अभियन्ता आरयूआईडीपी, जयपुर।
3. श्रीमान् उप कोषाधिकारी कुचामन।
4. श्रीमान् सहायक लेखाधिकारी कुचामन।
4. श्रीमान् अधिशाषी अभियन्ता आरयूआईडीपी, कुचामन।
5. श्रीमान् टीमलीडर सीएमसी-01 जयपुर।
6. श्रीमान् सहायक निर्माण अभियन्ता सीएमएससी-01।
7. कार्यालय रक्षित पत्रावली।


(अशोक कुमार जैन)
अधीक्षण अभियंता
आरयूआईडीपी, (पीआईयू) कुचामन

दिनांक - 11.9.2024


अधीक्षण अभियंता
आरयूआईडीपी, (पीआईयू) कुचामन

Kuchaman -Treasury Report of 5 APs


Advice No:114084

GA No.(Original Bill type) R
Month/Year:

Government of Rajasthan e-Advice for e-Kuber Rejected/Failed Transactions									
Budget Head : 8658-00-102-15-00									
Office Name : SE, RUIDP, Phase- IV, PIU- Kuchaman,					Office ID: 35878 DDO Code: 308962 TAN No.:				
To: The Treasury Officer, (Name) Please Order to pay Rs 47800 as per claim contained in this advice.									
S.No.	Employee Name Employee ID Nominee Name(S) Date of Death (only where Payment is made to Nominee) Third Party Name PAN No./TIN No./GSTIN No.	Correct Bank Details (To be filled by DDO) Name of Branch(Previous Branch Name) Bank Account No. (Previous Bank Account No.)	Original Bill NO Original Bill Date	Budget Head	Original Bill Reference ID	Original Token No	Challan No.	Net Amount	Remarks/Reject on Reason
1	Gopel Lal	KUCHAMAN CITY(STATE BANK OF INDIA) (KUCHAMAN CITY(STATE BANK OF INDIA)) 61260457680(61260437680)	52741778 10/09/2024	4217-60-050-07-01	52741778	2226281	31355	7100.00	Ac mismatch/ //RETURN FOR/RB(26924 12381565
2	Sundri Devi	KUCHAMAN CITY(CENTRAL BANK OF INDIA) (KUCHAMAN CITY(CENTRAL BANK OF INDIA)) 1533793052(1533763052)	52762736 11/09/2024	4217-60-050-07-01	52762736	2226283	30114	14700.00	ac mismatch/R03 ACCOUNT DOES NOT EXIST
3	Ramjan	Kuchaman City(PUNJAB NATIONAL BANK) (Kuchaman City(PUNJAB NATIONAL BANK)) 7558000100027548(7558000100027540)	52762736 11/09/2024	4217-60-050-07-01	52762736	2226283	30114	5700.00	ac mismatch/R03 ACCOUNT DOES NOT EXIST
4	Chauthi Devi	KUCHAMAN CITY(CENTRAL BANK OF INDIA) (KUCHAMAN CITY(CENTRAL BANK OF INDIA)) 3380015502(3580015502)	52762736 11/09/2024	4217-60-050-07-01	52762736	2226283	30114	14700.00	ac mismatch/R03 ACCOUNT DOES NOT EXIST
5	Rajni Munawat	KUCHAMAN CITY(Bandhan Bank) (KUCHAMAN CITY(Bandhan Bank)) 50190003606011(50090003606011)	52762745 11/09/2024	4217-60-050-07-01	52762745	2226284	30114	5700.00	ac mismatch/R03 ACCOUNT DOES NOT EXIST
Gross Amount: 47800									
Amount in Words : FOURTY SEVEN THOUSAND NINE HUNDRED ONLY									
Certificates: 1. Amount claimed in the Advice has not earlier been drawn. 2. Certified that I have personally examined and satisfied myself about the genuineness of claim that the e-kuber rejected/failed transactions of the Individual/Third party included in this advice are strictly in accordance with rules and that the said Individual/Third Party are entitled to such e-kuber rejected/failed transactions advice. It is further certified that I have personally ensured observance of all formalities regarding necessary entries. 3. It is certified that the Net claim of this advice will be transferred electronically into bank account of beneficiaries and Suspense Head in case unsuccessful payments(s) also that the correct bank detail(s) of the beneficiaries have been furnished in advice after due verification. 4. It is certified that I have carefully examined & verified the master data of the said claim.									
Sign of Clerk			Sign of Jr. ACTT./AO/ JUDV ACTT.			Sign (With Seal) is Sign/ Digital Sign of DDO /Administrator(s)			

Disclaimer: All contents related to this bill are provided by Head of Office/DDO and he/she is solely responsible for it.
 RAN National Informative Portal: Rajasthan State Information System (RSIS)

Print Date & Time : 23/10/2024 13:23:30

 Scanned with OKEN Scanner

I Certify that the Compliance of Directions/Instructions under the provisions of GF & AR has been ensured.			<u>Treasury Voucher</u> No. _____ Date: _____ <u>For Treasury Use</u>		
Sign (With Seal)/e-Sign/Digital Sign of DDO/Administrator(s)			Pay Rs. : 47900.00		
Admitted (RS.)			(In Words) : FORTY SEVEN THOUSAND NINE HUNDRED		
For Accountant General Office			(In Cash) : 47900.00		
Objected (RS.)			(In Words) : FORTY SEVEN THOUSAND NINE HUNDRED		
Auditor			Total Credit Rs.		
Supdt.			Auditor		
Gaz. officer			AAO-III		
			Treasury Officer		


Note :

1. In case of PD Account Budget Head, the PD Account No. should be displayed along with Budget Head.
2. All Fields are captured automatically from previous bill and challan generated by treasury except correction in Bank details.

PayManager
IFMS

Disclaimer: All contents related to this bill are provided by Head of Office/DDO and he/she is solely responsible for it.
 S/W National Informatics Centre, Rajasthan State Unit (<http://Paymanager.ra.nic.in>)

Print Date & Time : 23/10/2024 13:23:30

 Scanned with OKEN Scanner

Kuchaman –Payment receipt of 5 Aps

प्राप्ति रसीद


राजस्थान नगरीय आधारभूत विकास परियोजना (आरगूआईडीपी) चतुर्थ चरण के अन्तर्गत जल प्रदाय एवं सीवरज परियोजना कार्य के अन्तर्गत सड़कमण्डी, दुंगी रोड, एवं सीकर रोड के निम्नांकित बैंक खातों में ऑनलाईन/ मुआवजा राशि का हस्तान्तरण राशि प्रभावित व्यक्तियों के खातों में दिनांक 7/12/2024 को प्राप्त हो गई है।

क्र. सं.	आर पी सं.	प्रभावित व्यक्ति नाम	राशि	बैंक का नाम	खाता संख्या	हस्ताक्षर
1	169	Sundari Devi	14700	Central Bank of India	1533793052	
2	195	Ramjan	5700	Punjab National Bank	7558000100027548	रमजान
3	232	Raju Munawat	5700	Bandhan Bank	5019000360601	राजू
4	269	Chauthi Devi	14700	Central Bank of India	3380015502	
5	328	Gopal Lal	7100	State Bank of India	61260457680	गोपाल
Total			47900	Forty Seven Thousand Nine Hundred Only		



Appendix 3: Photograph of Identity Card Distribution to APs



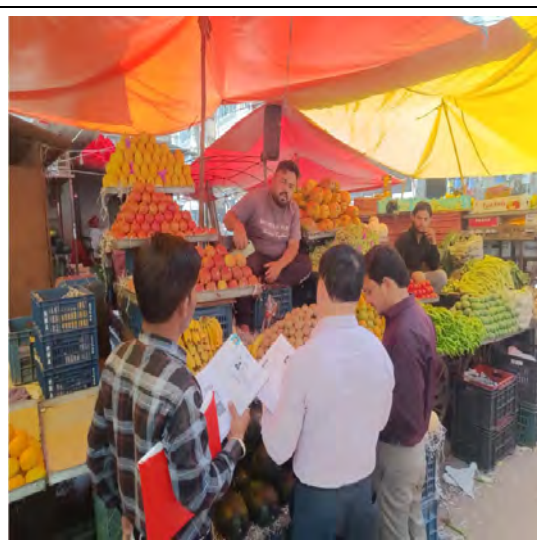

Appendix 4: Ward-wise population -Schedule Tribe towns**Town-wise population of ST households in Pratapgarh town**

Ward No.	Total Population	Scheduled Tribe Population	Percentage (%) of ST
1	154	22	14.29%
2	54	4	7.41%
3	168	66	39.29%
4	362	45	12.43%
5	518	86	16.60%
6	337	32	9.50%
7	223	52	23.32%
8	334	67	20.06%
9	370	59	15.95%
10	268	3	1.12%
11	568	19	3.35%
12	469	11	2.35%
13	372	0	0.00%
14	396	0	0.00%
15	73	0	0.00%
16	238	2	0.84%
17	748	3	0.40%
18	387	4	1.03%
19	218	2	0.92%
20	297	1	0.34%
21	337	2	0.59%
22	182	2	1.10%
23	448	11	2.46%
24	696	11	1.58%
25	179	2	1.12%
26	351	39	11.11%
27	243	40	16.46%
28	17	0	0.00%
29	135	6	4.44%
30	115	14	12.17%
31	245	28	11.43%
32	69	2	2.90%
33	545	17	3.12%
34	344	8	2.33%
35	351	79	22.51%
36	116	10	8.62%
37	141	23	16.31%
38	576	53	9.20%
39	84	6	7.14%
40	187	29	15.51%
	11915	860	7.22%

Ward-wise population of ST households in Banswara town

Ward No.	Total Population	Scheduled Tribe Population	Percentage (%) of ST
1.	3285	1751	53.30%
2.	5033	219	4.35%
3.	3089	416	13.47%
4.	1584	56	3.54%
5.	830	13	1.57%
6.	3515	237	6.74%
7.	3288	718	21.84%
8.	3028	46	1.52%
9.	2885	263	9.12%
10.	2544	192	7.55%
11.	2420	56	2.31%
12.	3810	753	19.76%
13.	2815	3	0.11%
14.	2455	846	34.46%
15.	2756	142	5.15%
16.	3612	508	14.06%
17.	3077	125	4.06%
18.	2370	47	1.98%
19.	4689	323	6.89%
20.	2549	370	14.52%
21.	2603	358	13.75%
22.	1630	9	0.55%
23.	1416	1	0.07%
24.	859	6	0.70%
25.	831	0	0.00%
26.	1756	9	0.51%
27.	1313	6	0.46%
28.	1258	9	0.72%
29.	1199	123	10.26%
30.	1509	27	1.79%
31.	2515	202	8.03%
32.	3143	1205	38.34%
33.	1974	11	0.56%
34.	3095	4	0.13%
35.	1899	16	0.84%
36.	870	3	0.34%
37.	1401	14	1.00%
38.	3071	389	12.67%
39.	3356	183	5.45%
40.	4637	364	7.85%
41.	1048	34	9.96%
	101017	10057	53.30%

Ward-wise population of ST households in Abu Road Town

Ward No.	Total Population	Scheduled Tribe Population	Percentage (%) of ST
1	3071	103	3.35%
2	1191	463	38.87%
3	2356	322	13.67%
4	1544	122	7.90%
5	2181	251	11.51%
6	1317	130	9.87%
7	1420	105	7.39%
8	1300	87	6.69%
9	1140	119	10.44%
10	925	27	2.92%
11	1411	58	4.11%
12	1283	1	0.08%
13	1160	25	2.16%
14	2095	50	2.39%
15	1754	15	0.86%
16	1341	18	1.34%
17	1928	78	4.05%
18	1699	39	2.30%
19	1187	393	33.11%
20	2758	243	8.81%
21	1704	67	3.93%
22	1652	475	28.75%
23	1522	88	5.78%
24	2120	267	12.59%
25	2293	108	4.71%
26	1769	166	9.38%
27	757	57	7.53%
28	3577	279	7.80%
29	1880	334	17.77%
30	2028	264	13.02%
31	3236	760	23.49%
	55599	5514	9.92%

Appendix 5: Photographs of civil work under FSSM towns

Town Name	Location
FSTP construction at Tijara (Alwar)	
FSTP construction at Deeg (Bharatpur)	
FSTP construction at Bari (Dhaulpur)	

<p>FSTP construction at Dausa</p>	 <p>A photograph of a single-story building under construction with orange and white walls. A black ladder is leaning against the right side of the building. A black plastic chair is on the ground in front of the building. The image includes a Google Maps inset and a GPS overlay.</p> <p>Rohara, Rajasthan, India W8x9+mq, Rohara, Rajasthan 303303, India Lat 26.949182° Long 76.319262° 24/03/25 10:16 AM GMT +05:30</p>
<p>FSTP construction at Bhawani Mandi (Jhalawar)</p>	 <p>A photograph of a single-story building under construction with grey concrete walls. In the foreground, there are large blue cylindrical pipes lying on the ground. The image includes a Google Maps inset and a GPS overlay.</p> <p>Jhalawar, Rajasthan, India Rajasthan 326512, India, Jhalawar, Rajasthan 326512, India Lat 24.390938° Long 75.7945° 24/03/2025 10:56 AM GMT +05:30</p>
<p>FSTP construction at Neem Ka Thana (Sikar)</p>	 <p>A photograph of a single-story building under construction with orange and white walls. A solar panel is mounted on the roof. A black plastic chair is on the ground in front of the building. The image includes a GPS overlay.</p> <p>GPS Map Camera Lite</p>

<p>FSTP construction at Bandikui (Dausa)</p>	
<p>FSTP construction at Jobner (Jaipur)</p>	
<p>FSTP construction at Gangapur (Bhilwara)</p>	 <p>Delana Rural, Rajasthan, India 66cv+vh, Delana Rural, Rajasthan 311801, India Lat 25.223806° Long 74.244715° 03/04/2025 03:23 PM GMT +05:30</p>

<p>FSTP construction at Shahpura (Bhilwara)</p>	
<p>FSTP construction at Pilibanga (Hanumangarh)</p>	
<p>FSTP construction at Kanor-Bhinder (Udaipur)</p>	

Appendix 6: Photograph of consultation with stakeholders and community

Public consultations organized with project affected persons as well as local public and following issues were discussed.

- Present status and access of Water Supply and Waste Water in the town and other concerned issues and challenges
- process of logging complaints and grievance and its mechanism under the project
- Willingness of local public to pay for improved services.

Outcome: Pamphlet of advance information is distributed and door to door consultation is also held with nearby habitations. Three tier grievance mechanisms and its process was briefed with participants. People are supportive of the project and indicated their willingness to participate in the project to make it successful and are willing to pay for the improved quality of water and sewerage connections. People are not satisfied with present water supply and sewerage services, water is provided by PHED but its intermittent on alternate days and sewerage facility is not structured in the town. People are happy and understand direct benefits along with latent benefits of the project.





Consultation in Khetri



Consultation in Ladnu



Consultation in Didwana



Consultation in Kuchaman



Consultation in Mandawa



Sample copy of Attendance sheet

Community Awareness and Public Participation Capp, RUIDP-Phase-IV
Consultation Sheet

Project Town:-Kuchaman City Name Of Colony:- 1200th CWK, Panchsheel

Date: 27/03/2025 Name Of Activity:- Meeting with women

Attendance Sheet

Sr. No.	Name	Contact No.	Occupation	Signature
1	Abhinav Nandani	9650627566	LET	[Signature]
2	Anees	9351652007		[Signature]
3	Hemraj	8928864189		[Signature]
4	Raj			[Signature]
5	Chandran			[Signature]
6	Linessh		Safety	[Signature]
7	Ramraj Cal			[Signature]
8	Tajpal			[Signature]

RUIDP
(A Unit of RUDSICO)

Rajasthan Secondary Towns Development Sector Project (RSTDSP)
RUIDP Phase-IV
Contract Management and Supervision Consultant (CMSC-01)

Labour Consultation & Site Safety Training
Attendance Sheet

Place: SIF 2.0 MID Bidwara Town, Date: 27.08.2025

Topic/Issues Discussed: Labour Consultation with meeting regarding workers working time use of PPE kit & Health measures during work at Bidwara Town.

Sl. No.	Name	Gender		Occupation	Mobile No.	Signature
		Male	Female			
1	Bal Ram Pailoon	✓		Hand	9285059198	[Signature]
2	Sarma		✓	"		[Signature]
3	Soni Patel	✓		"		[Signature]
4	Asit Ram	✓		"		[Signature]
5	Shahrukh	✓		"	7742096701	[Signature]
6	Munesh	✓		"		[Signature]
7	Vinod	✓		"		[Signature]
8						
9						
10						
11						
12						
13						
14						
15						

M=06
F=01
Total

[Signature]
Social Safeguard Support Staff
CMSC-01, Ladnun



Community Awareness and Public Participation-CAPP, RUIDP-Phase-IV
Consultation Sheet

Name of Project town: सुपारा Date: 13-02-25 Ward No: 01
Name of Colony/Landmark: डिवाली रोड Name of Activity: घुवा मीटिंग


Issues covered:-

1. Consultation before start of work & Temporary inconvenience
2. Project details and benefits
3. Labour Safety, Health & Hygiene
4. Grievance Redressal
5. New water connection
6. Benefit of water metering
7. Pamphlets Distribution
8. Sewer connection
9. BPL connection verification
10. Operation & Maintenance/ CRM/ Toll Free
11. Any other issue (specify)*

S.No.	Name	Address/Designation	Sex		Mobile No.	If BPL family (Card Number)	Issue discussed *(Write the issues covered as mentioned above)	Signature	Remarks
			M	F					
1-	गोपाल	डिवाली रोड	✓		9549890 630		02, 05, 08	गोपाल	
2-	पवन	— // —	✓				— // —	पवन	
	जिनेन्द्र	— // —	✓				— // —		
3	प्रवीण	— // —	✓				— // —		
4-	गुण	— // —	✓				— // —		
5	हरिन्द	— // —	✓				— // —	नरेश	
6	नरेश	— // —	✓		869652 8646		— // —		
7	अजय कर्वा	— // —	✓				— // —		
8	अजय सिंह	— // —	✓			सामाजिक विकास विशेषज्ञ केंद्र	— // —		
9	शशि	— // —	✓			सुधान	— // —		
10	गुण	— // —	✓				— // —		



Shot on OnePlus
Jai shree Ram





Rajasthan Secondary Towns Development Sector Project (RSTDSP)
RUIDP Phase-IV
Contract Management and Supervision Consultant (CMSC-01)

Activity: Site Safety Training Program
Attendance Sheet


Place: STP- 3.0 m/s diaphragm Date: 28/02/2025
 Topic/Issues Discussed:

Labour Consultation with meeting regarding
 Safety measures and health care during working
 time.

Sl.	Name	Gender		Occupation	Mobile No.	Signature
		Male	Female			
1	दीपक शर्मा	✓		labour	8052493977	
2	पिन्टू माडन	✓		"	7766044874	
3	अमरजीत	✓		"	7763934632	
4	निपिन	✓		"	9122914662	
5	विमल	✓		"	8002729742	
6	विमल शर्मा	✓		"	—	
7	राजेश माडन	✓		"	9955633371	
8	रविश माडन	✓		"	—	
9	राजेश माडन	✓		"	—	
10	दीप		✓	"	9285059198	
11	राजेश		✓	"	—	
12						
13						
14						
15						

M = 9
 F = 2
 Total = 11

Monica
 29/02/2025
 Social Safeguard
 support staff




Community Awareness and Public Participation-CAPP, RUIDP-Phase-IV
Consultation Sheet

RUIDP
(A Unit of RUIDSICO)

Name of Project town: Khetri Date: 15-12-24 Ward No: 24
Name of Colony/Landmark: Police chhatri Name of Activity: DOOR TO DOOR NEW WATER CONN.
Issues covered: NEW WATER CONN.

1. Consultation before start of work & Temporary inconvenience
2. Project details and benefits
3. Labour Safety, Health & Hygiene
4. Grievance Redressal
5. New water connection
6. Benefit of water metering
7. Pamphlets Distribution
8. Sewer connection
9. BPL connection verification
10. Operation & Maintenance/ CRMC/Toll Free
11. Any other issue (specify)*

S.No.	Name	Address/Designation	Sex		Mobile No.	If BPL family (Card Number)	Issue discussed *(Write the issues covered as mentioned above)	Signature	Remarks
			M	F					
1	राजेश सिंह	विमान-4 गार्ड	✓		992824 9283		S, 8, 11	21/11/24	
2	राजेश कुमार	"	✓		950930 1464		S, 8, 11	21/11/24	
3	प्रियम सिंह	"	✓		946100 2030		S, 8, 11	P.S	
4	राज सिंह	"	✓		830209 100		S, 8, 11	21/11/24	
5	विकास सिंह	"	✓		830509 993		S, 8, 11	B.S	
6	प्रियम सिंह	"	✓		946100 2030		S, 8, 11	P.S	
7	पुष्प सिंह	"	✓		830209 100		S, 8, 11	21/11/24	
8	अरुण सिंह	"	✓		9413569 985		S, 8, 11	21/11/24	
9	बजरंग प्रसाद	"	✓		950930 1464		S, 8, 11	21/11/24	
10	देवी सिंह	"	✓		830509 993		S, 8, 11	21/11/24	



Community Awareness and Public Participation-CAPP, RUIDP-Phase-IV

Consultation Sheet

Name of Project town: Khetri Date: 11/11/24 Ward No: 02
 Name of Colony /Landmark: खोली धाट Name of Activity: Door To Door

Issues covered: -

- | | | |
|----------------------------------------------------------------|---------------------------------|------------------------------------|
| 1. Consultation before start of work & Temporary inconvenience | 2. Project details and benefits | 3. Labour Safety, Health & Hygiene |
| 4. Grievance Redressal | 5. New water connection | 6. Benefit of water metering |
| 7. Pamphlets Distribution | 8. Sewer connection | 9. BPL connection verification |
| 10. Operation & Maintenance/ CRMC/Toll Free | 11. Any other issue (specify)* | |

S.No.	Name	Address/Designation	Sex		Mobile No.	If BPL family (Card Number)	Issue discussed *(Write the issues covered as mentioned above)	Signature	Remarks
			M	F					
	बालुलाल	खोली धाट	✓		8742857793		S, G, 9		
	लीलाराम	खोली धाट	✓		9602097059		S, G, 9		
	सतोप कुमार	खोली धाट	✓		8002824042		S, G, 9		
	इन्द्रराम	खोली धाट	✓		9650181866		S, G, 9		
	मधवीर प्रसाद	खोली धाट	✓		9785467043		S, G, 9		
	जगदीश लाल	खोली धाट	✓		6376089771		S, G, 9		
	पताराजी डेवी	खोली धाट		✓	9672439875		S, G, 9		
	पूरनमल	खोली धाट	✓		8559940507		S, G, 9		
	फाजुराम	खोली धाट	✓		9785807284		S, G, 9		
	मुकेश कुमार	खोली धाट	✓		9920901201				

Community Awareness and Public Capp, RUIDP- Ph-IV
Consultations Sheet

Project Town: Kumbhgarh city Name Of Colony: Kumbhgarh Nagar Colony
Date: 22-11-2024 Name of Activity: Public Consultation

Attendance Sheet

S.N.	Name	Occupation	Mobile Number	Signature
1	राधा देवी		9660499285	राधा देवी
2	शंकर लाल		9680935380	
3	महेश प्रकाश		9799302500	
4	अनिल देवी		9732330842	
5	निजेश कुमार		9432832594	
6	आमराज मीना			गुणल राम
7	गुणल राम			
8	धुषा शर्मा			
9	मन्मथी लाल			
10	लीला क शर्मा			
11	रत्ना कर्मा		8079008831	
12	शमन्दर सिंह			
13	इन्द्रा देवी		8829761702	-सिद्धा
14	वैकिश			
15	देवी लाल			
16	प्राणुराम			
17	पाना राम			
18	काशु देवी			गिरधारी
19	गिरधारी			
20	मंजरी			

Community Awareness and Public Participation-CAPP, RUIDP-Phase-IV
Consultation Sheet

RUIDP
(A Unit of HUDCO)

Name of Project town: HOS/17 Date: 30/11/24 Ward No. STP
Name of Colony / Landmark: Pratish S/S Name of Activity: meeting with Project Labour

Issues covered:-

1. Consultation before start of work & Temporary Inconveniences
2. Project details and benefits
3. Grievance Redressal
4. New water connection
5. Pamphlets Distribution
6. Sewer connection
7. Operation & Maintenance/ CRMC/Toll free
8. Any other issue (specify)*
9. Labour Safety, Health & Hygiene
10. Benefit of water metering
11. RPL connection verification

S.No.	Name	Address/Designation	Sex		Mobile No.	If BPL Family (Card Number)	Issue discussed (*With checkboxes covered as mentioned above)	Signature	Remarks
			M	F					
1.	महाध	ग्रामिक	✓				3, 11		
2.	मोहन लाल	"		✓			3, 11		
3.	जीती	"		✓			3, 11		
4.	लालकृष्ण	"		✓			3, 11		
5.	श्रीकृष्ण	"	✓				3, 11		
6.	मोहन	"	✓				3, 11		
7.	रामचरण	"	✓				3, 11		
8.	जीती लाल	"		✓			3, 11		
9.	लालकृष्ण	"	✓				3, 11		
10.	युवा	"		✓			3, 11		

RUIDP
Rajasthan Urban Infrastructure Development Project

Community Awareness and Public Participation-CAPP, RUIDP-Phase-IV

Consultation Sheet

Name of Project town: Ladnun Date: 07-01-2015 Ward No: Small Group meeting

Name of Colony/Localities: Ramdev Colony Name of Activity: Small Group meeting

Issues covered:-

1. Consultation before start of work & Temporary inconvenience
2. Project details and benefits
3. Latrine Safety, Hygiene & Hygiene
4. Grievance Redressal
5. New water connection
6. Benefits of water metering
7. Fairness in Distribution
8. Sewer connection
9. BPL connection verification
10. Operation & Maintenance/ CHQ/Toll free
11. Any other issue (specify)

S.No.	Name	Address/Designation	Sex		Mobile No.	H BPL family (Card Number)	Issue discussed (write the issue covered in warden's sheet)	Signature	Remarks
			M	F					
1	205/11	3119 मीरठा		✓	-	-	2,9	-	
2	206/11	3119 मीरठा		✓	-	-	2,9	-	
3	211/11	3119 मीरठा		✓	-	-	2,9	-	
4	11 कमीरठा	3119 मीरठा	✓		819011314	-	2,9	-	
5	11/11	3119 मीरठा	✓		-	-	2,9	-	

Community Awareness and Public participation Capp,RUIDP-Phase-1V

Project Town.....

Consulation Sheet

Name Of colony:.....Mehrauli Dhanu

Date:.....18-10-2024

Name of Activity:.....Gram Grouh Discuss

Attendance Sheet

S.N.	Name	Occupation	Mobile Number	Signature
1	पुष्पिका			
2	राम राम		9460776882	
3	भावणी देवी			
4	महावीर		9667606186	
5	गणेश मिश्र		966775608	गणेश मिश्र
6	परमेश्वरी देवी		9982375378	
7	पिकी कंवर			पिकी कंवर
8	मैना देवी			
9	लिमला देवी			लिमला देवी
10	सरी ज			
11	किशन कंवर		9929371102	
12	राम कामता		889442335	
13	सुमन			
14	आका म			
15	दीपिका			
16	संगीता देवी			
17	आविषी देवी			
18	नीजा देवी		9413928587	नीजा देवी
19	समीता देवी			
20	कविता देवी		998201855	



Community Awareness and Public Participation-CAPP, RUIDP-Phase-IV

Consultation Sheet

Name of Project town: Date: 25/11/2024 Ward No: 01

Name of Colony/Landmark: डीना की हार्ड Name of Activity: Door To Door BPL Connection

Issues covered:

1. Consultation before start of work & Temporary inconvenience
2. Project details and benefits
3. Labour Safety, Health & Hygiene
4. Grievance Redressal
5. New water connection
6. Benefit of water metering
7. Pamphlet Distribution
8. Sewer connection
9. BPL connection verification
10. Operation & Maintenance/ CRM/ Toll Free
11. Any other issue (specify)*

S.No.	Name	Address/Designation	Sex		Mobile No.	If BPL family (Card Number)	Issue discussed (Write the issues covered as mentioned above)	Signature	Remarks
			M	F					
	तीरथचंद	डीना की हार्ड	✓		461228388		5, 8, 9	तीरथचंद	
	विजय लाल	डीना की हार्ड	✓		8894543190		5, 8, 9	विजय	
	बाला देवी	डीना की हार्ड	✓		8850765062		5, 8, 9	बाला देवी	
	रेवती अग्रवाल	डीना की हार्ड	✓		9314885006		5, 8, 9	रेवती	
	आमिरा	डीना की हार्ड	✓		957183211		5, 8, 9	आमिरा	
	मिशोरी लाल	डीना की हार्ड	✓		8719047092		5, 8, 9	मिशोरी	
	अशुभर	डीना की हार्ड	✓		807465076		5, 8, 9	अशुभर	
	अनारसी देवी	डीना की हार्ड	✓		807458346		5, 8, 9	अनारसी देवी	
	मोहन कुमार	डीना की हार्ड	✓		917202360		5, 8, 9	मोहन	
	रामेश	डीना की हार्ड	✓		756840088		5, 8, 9	रामेश	

RUDP
Rajasthan Urban Development Project

Community Awareness and Public Participation-CAPP, RUDP-Phase-V
Consultation Sheet

Name of Project town:- NEST Date: 12/1/18 Ward No: 11
Name of Colony / Landmark:- SECTOR 12 Name of Activity: Survey for Water Connection
Group formed:-

1. Consultation before start of work & whenever necessary
2. Project details and benefits
3. Local facility, credit & support
4. Drinking water connection
5. Beneficiary list & water mapping
6. People's Committee
7. Technical service
8. PH. covered on completion
9. Operation & Maintenance/ O&M Cell
10. Any other issue (specify)

S.No.	Name	Address/Designation	Sex	Mobile No.	IFPI family (Circ number)	Issue discussed (Write the consultation in Hindi/English)	Signature	Remarks
			M	F				
1.	मन्नु मीठा	विकासी		W		2, 4, 5, 6		
2.	शुद्धे कुमर	"		W	93569498	"		Shruti
3.	शैलू जगद	"		W	93945303	"		Shruti
4.	धनर रत	"		W	93945303	"		Shruti
5.	माया शै	"		W		"		
6.	मैना शै	"		W		"		
7.	मैना शै	"		W	93945303	"		Shruti
8.	मैना शै	"		W		"		
9.	मैना शै	"		W	93945303	"		Shruti

[illegible]

[illegible]

Appendix 7: Photographs of activities performed under Gender Action Plan**Door to door consultation****Water Audit**



FGD





Orientation Meeting with Women Ward Councillor



School Student Awareness at Kuchaman



FGD at Makrana

जल संरक्षण : शुद्ध पेयजल एक प्रतिशत से भी कम बचा है : चंदेल

पानी पर हक है हमारा फिल्म का
किता प्रदर्शन, बच्चों को पाने
को बचा, स्वच्छ व स्वच्छता
के लिए किता प्रोत्साहित

नवीनदी-सिरोही।

राजस्थान नवीनदी आधुनिक विकास कोष के जल संरक्षण कार्यक्रम के तहत चंदेल में जल संरक्षण पर फिल्म दिखाने व विद्यार्थियों को जल को बचाने की जानकारी दी। जल संरक्षण कार्यक्रम के तहत चंदेल में जल संरक्षण पर फिल्म दिखाने व विद्यार्थियों को जल को बचाने की जानकारी दी। जल संरक्षण कार्यक्रम के तहत चंदेल में जल संरक्षण पर फिल्म दिखाने व विद्यार्थियों को जल को बचाने की जानकारी दी।

10 बच्चों ने किता जल अकेला

राजस्थान नवीनदी आधुनिक विकास कोष के जल संरक्षण कार्यक्रम के तहत चंदेल में जल संरक्षण पर फिल्म दिखाने व विद्यार्थियों को जल को बचाने की जानकारी दी। जल संरक्षण कार्यक्रम के तहत चंदेल में जल संरक्षण पर फिल्म दिखाने व विद्यार्थियों को जल को बचाने की जानकारी दी। जल संरक्षण कार्यक्रम के तहत चंदेल में जल संरक्षण पर फिल्म दिखाने व विद्यार्थियों को जल को बचाने की जानकारी दी।

छात्रों को बताए पानी बचाने के उपाय, 'पानी पर हक है हमारा' डॉक्युमेन्टरी फिल्म दिखाई

सिरोही में राजस्थान नवीनदी आधुनिक विकास परियोजना की सामुदायिक जागरूकता एवं जनसहभागिता इकाई का आयोजन

सिरोही। राजस्थान नवीनदी आधुनिक विकास परियोजना की सामुदायिक जागरूकता एवं जनसहभागिता इकाई की ओर से सिरोही में डॉक्युमेन्टरी फिल्म 'पानी पर हक है हमारा' का प्रदर्शन किया गया। कार्यक्रम में पानी के महत्व पर बच्चों को शिक्षित करने के लिए राजस्थान नवीनदी आधुनिक विकास परियोजना की ओर से सिरोही में डॉक्युमेन्टरी फिल्म 'पानी पर हक है हमारा' का प्रदर्शन किया गया। कार्यक्रम में पानी के महत्व पर बच्चों को शिक्षित करने के लिए राजस्थान नवीनदी आधुनिक विकास परियोजना की ओर से सिरोही में डॉक्युमेन्टरी फिल्म 'पानी पर हक है हमारा' का प्रदर्शन किया गया।



जयपुर टाइम्स

जयपुर (Jodhpur) 10th June 2023 - Page 8

जल संरक्षण के लिए जागरूकता पर जोर

जयपुर, राजस्थान। राजस्थान नवीनदी आधुनिक विकास परियोजना की सामुदायिक जागरूकता एवं जनसहभागिता इकाई की ओर से जयपुर में डॉक्युमेन्टरी फिल्म 'पानी पर हक है हमारा' का प्रदर्शन किया गया। कार्यक्रम में पानी के महत्व पर बच्चों को शिक्षित करने के लिए राजस्थान नवीनदी आधुनिक विकास परियोजना की ओर से जयपुर में डॉक्युमेन्टरी फिल्म 'पानी पर हक है हमारा' का प्रदर्शन किया गया।

Appendix 8: Copy of office order of PMU for follow grievance mechanism agreed with ADB

Government of Rajasthan
Office of Project Director
Rajasthan Urban Infrastructure Development Project (Unit of RUDSICO)

AVS Building, Jawahar Circle, JLN Marg, Jaipur - 302017
 Tel No.: 0141-2721988, Fax No.: 0141-2721919,
 email: mainruidp@gmail.com, mail.ruidp@rajasthan.gov.in, web site : www.ruidp.org.in/ruidp
 No. F3 (301) (60)/RUIDP/PMU/PH-IV/ADB S. Safeguard /Gen adm./2020-21/11364. Date: 21/12/20

Suprintending Egnieer/Executive Engineer
 PIU- Abu Road, Sirohi, Ratangarh,
 Fatehpur, Lakmangarh, Sardarsahar,
 Kuchaman, Lachnu, Mokrana, Didwana,
 Khetri, Mandawa, Pratapgarh and
 Banswara.

Subject:- Nomination of Safeguard and Safety Officer (SSO) of each PIUs for proper monitoring of Environmental and Resettlement issues and addressing of safeguard related Grievances through Grievance Redress Mechanism.

Reference:- Agreed Environmental Resettlement framework and EARF of RSTDSP.

All PIUs are directed to issue an office order to nominate one engineer from PIU to works as Safeguard and Safety Officer (SSO). It will be additional responsibility of Safeguard and Safety Officer (SSO), PIU to ensure day to day monitoring of implementation of Environmental Management and Monitoring Plan (EMMP) provisions, implementation & Monitoring Resettlement Plan (RP) and ADB Safeguard Policy & Safety compliance in concern town.

Further it is directed that all the PIU should maintain proper separate records of safeguard related Grievances received in their town and ensure that the safeguard related Grievances received are resolved as per Grievance Redress Mechanism (GRM) prescribed in EARF/RF which is summarized as under (for ready reference)

Methodology of multi-tier GRM	Responsibility/Action to be taken	Time Frame	Record Keeping
1st Level: Grievances that are immediate and urgent in the perception of the complainant, the contractor, and supervision personnel from PIU and CMSC on-site will provide the most easily accessible or first level of contact for quick resolution of grievances	1st: PIU will resolve issues in consultation with supervision personnel (ACM), Safeguard and Safety Officer (SSO) PIU, Contractor, and Safeguard staff of CMSC. If required, city level monitoring committee (CLMC) will be involved in resolution of grievances at the 1st level.	PIU will resolve issues within 7 days of receipt of a complaint/ grievance	Safeguard Support of CMSC will oversee the matters and prioritize / follow up the issues with PIU/Contractor. Safeguard and Safety Officer of PIUs, Safeguard Support of CMSC will record Grievances timely in the format enclosed as Annexure 1. Contractor/ Safeguard Support of CMSC will enter the general Grievance received (in a summarized manner) in Grievance Register (format enclosed as Annexure 2) on receipt form public forwarded to head of PIU or Safeguard and Safety Officer (SSO) for resolve in time and provide summarized information as and when require. The grievance register will be endorsed by all field agencies involved in implementation of EMP and

Project Librarian/Project File Copying Building
 Received by: 21/12/2020
 Inward No: 1 P.C

TE	AC	SC	CC
AT	UE	IT	CC
SC	UE	IT	CC


Methodology of multi-tier GRM	Responsibility/Action to be taken	Time Frame	Record Keeping
2nd level: All grievances that cannot be redressed within 7 days at field/PIU level will be brought to the notice of Zonal PIU headed by Additional Chief Engineer (ACE).	The ACE at zonal PIU will resolve issues in consultation with SE/EE PIU, assistant safeguard officer (ASO), field level PIU, CMSC, and the contractor.	The ACE at zonal PIU will resolve the grievance within 7 days of receipt of complaint/grievance.	Environmental and Social Safeguards Personal of CMSC will keep all the records referred to zonal PIU and after compilation, all the details will be submitted to PMU.
3rd level: All the grievances that are not addressed by Zonal PIU within 7 days of receipt will be brought to the notice of the PMU.	Project Officer (Social/Environment) at PMU will resolve the grievances with necessary coordination of Zonal PIU and CMSC and guidance/instruction of additional project director (APD-PMU).	PMU will resolve the grievance within 15 days of receipt of grievance.	Safeguard Support of PMCBC will keep all the records referred to PMU.
4th level: Grievances not redressed through this process within stipulated time period will be referred to the CLC/grievance redress committee (GRC).	Zonal PIU will inform the CLC regarding any grievances required to be resolved urgently.	The GRC will resolve the grievance within 15 days of resolving the complaint.	Environmental and Social Safeguards Personal of CMSC will keep all the records.

Please note that an aggrieved person shall have access to the country's legal system at any stage, and accessing the country's legal system can run parallel to accessing the GRM and is not dependent on the negative outcome of the GRM.

PIU Safeguard and Safety Officer (SSO) will monitor the entire process and all decisions taken by the PIU, zonal officers, PMU and GRC and will be communicated to the APs by Safeguard Support of CMSC.

It is also directed that names and contact number of the concerned Safeguard and Safety Officer (SSO) of PIU, contractors, safeguard support staff of CMSC will be posted at all construction sites at visible locations.


All PIUs will ensure timely issuance of order with a copy to Project Officer (Social & Environment), PMU. Further PIUs will be responsible to ensure redressal of grievances as per GRM procedures summarized above.


 Chief Engineer, RUIDP

No. F3 (301) (80)/RUIDP/PMU/PH-IV/ Social Safeguard/General Adm./2020-21/ Date: 18/12/2020

Copy to the following for information and necessary action please:- 18369-76

1. ACE-I & II Phase-IV, RUIDP zone Jaipur & Jodhpur
2. TL, PMCBC, Phase-IV, RUIDP
3. TL CMSC-01/02 Phase-IV, RUIDP zone Jaipur & Jodhpur


 18/12/2020
 (K. M. Mandiwala)
 PO (Co-ord. & Social)

RUIDP Phase-IV: Consultants Page 2 of 2
